

Orange County Public Schools





Welcome! Please sign in
on your mobile device:
<http://communitymeeting.ocps.net/>



Hungerford Elementary School
40% Construction Community Meeting
February 12, 2018

Hungerford Elementary School Replacement Meeting Agenda

February 12, 2018 6:00 PM

- Welcome – School Board Member: Nancy Robinson
- Introductions – Jessma Lambert, Facilities Planning Director
- Project Update – Architect: 
Contractor: 
- Questions and Answers
- Adjournment


Orange County Public Schools



Orange County Public Schools




Orange County Public Schools

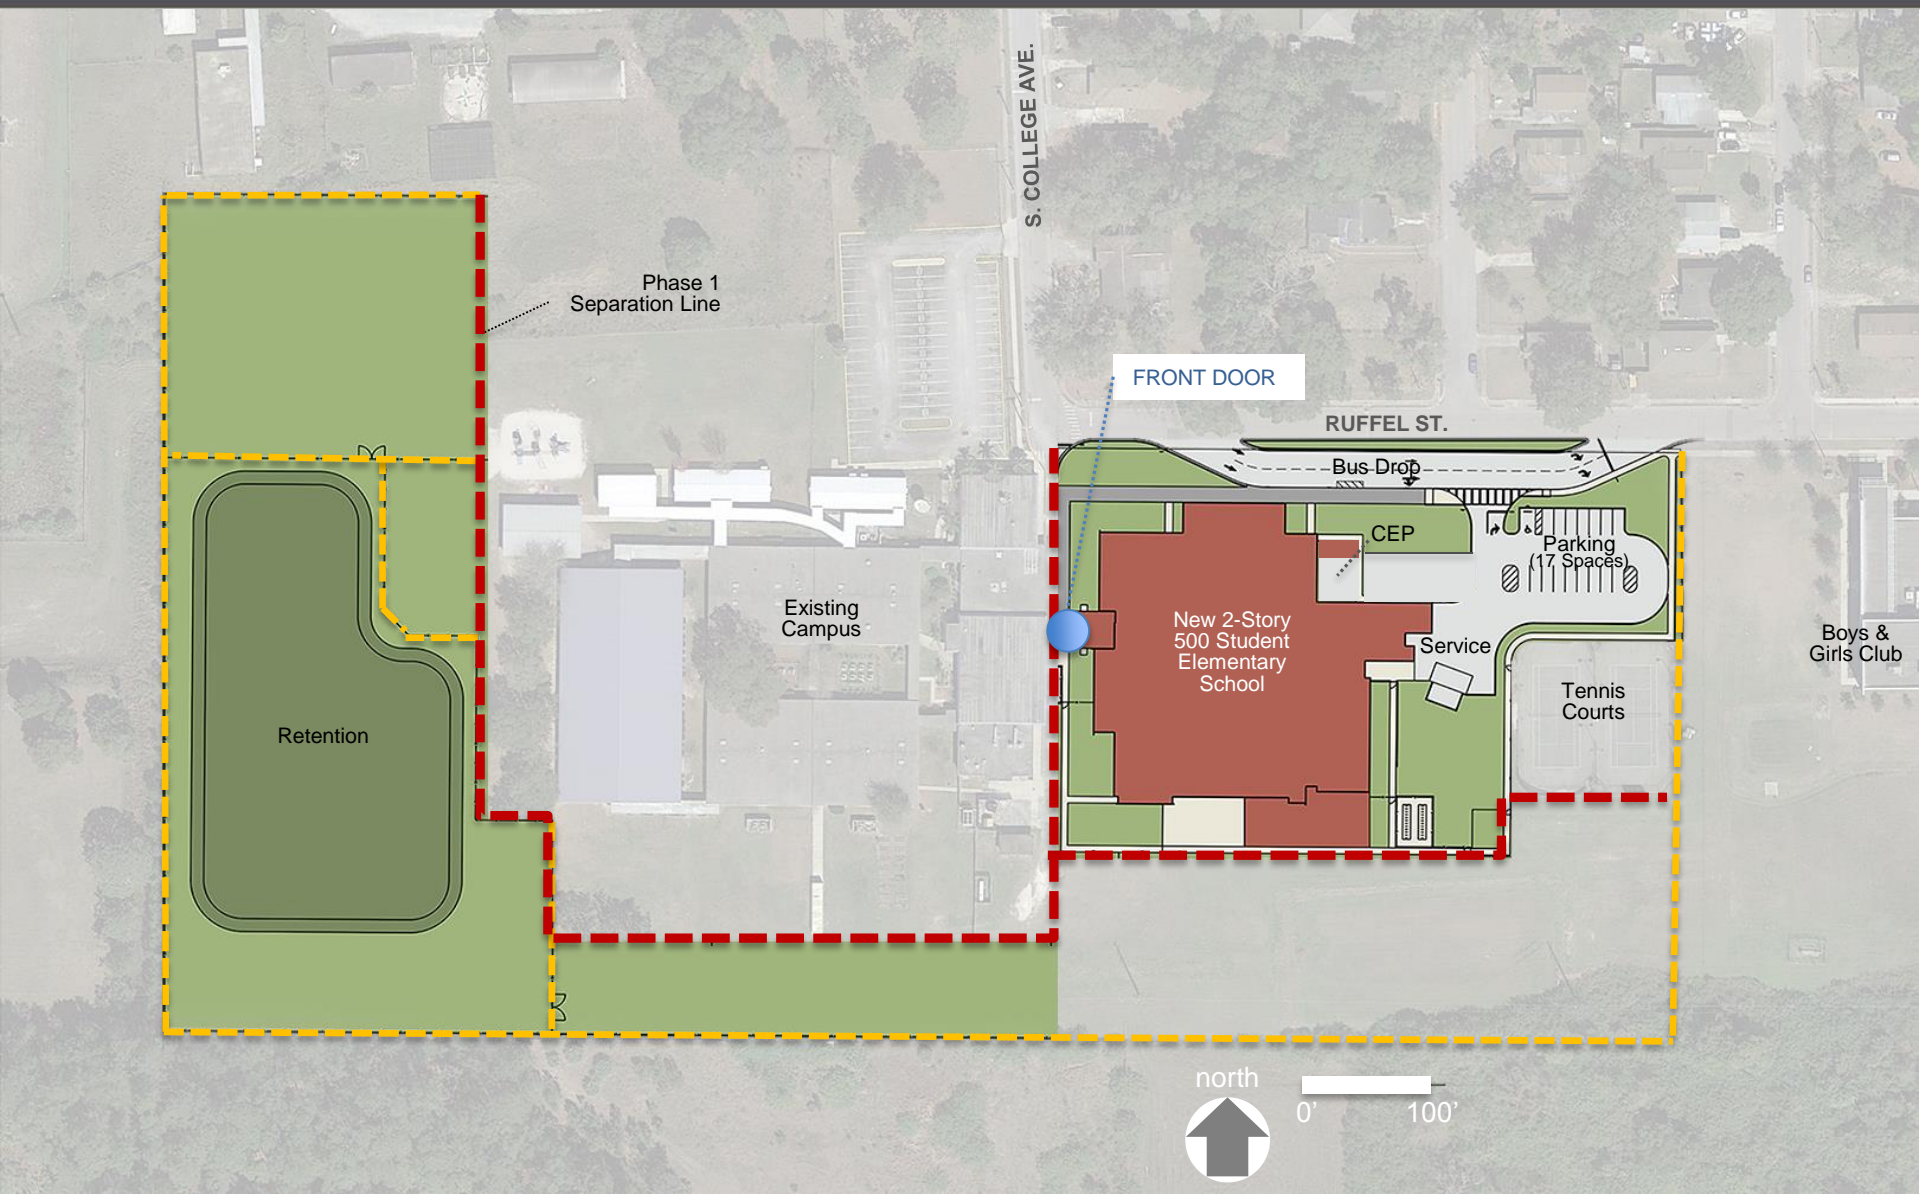

Site Plan – PHASE 1 – New School, play amenities, service, staff parking, and retention pond

Orange County Public Schools

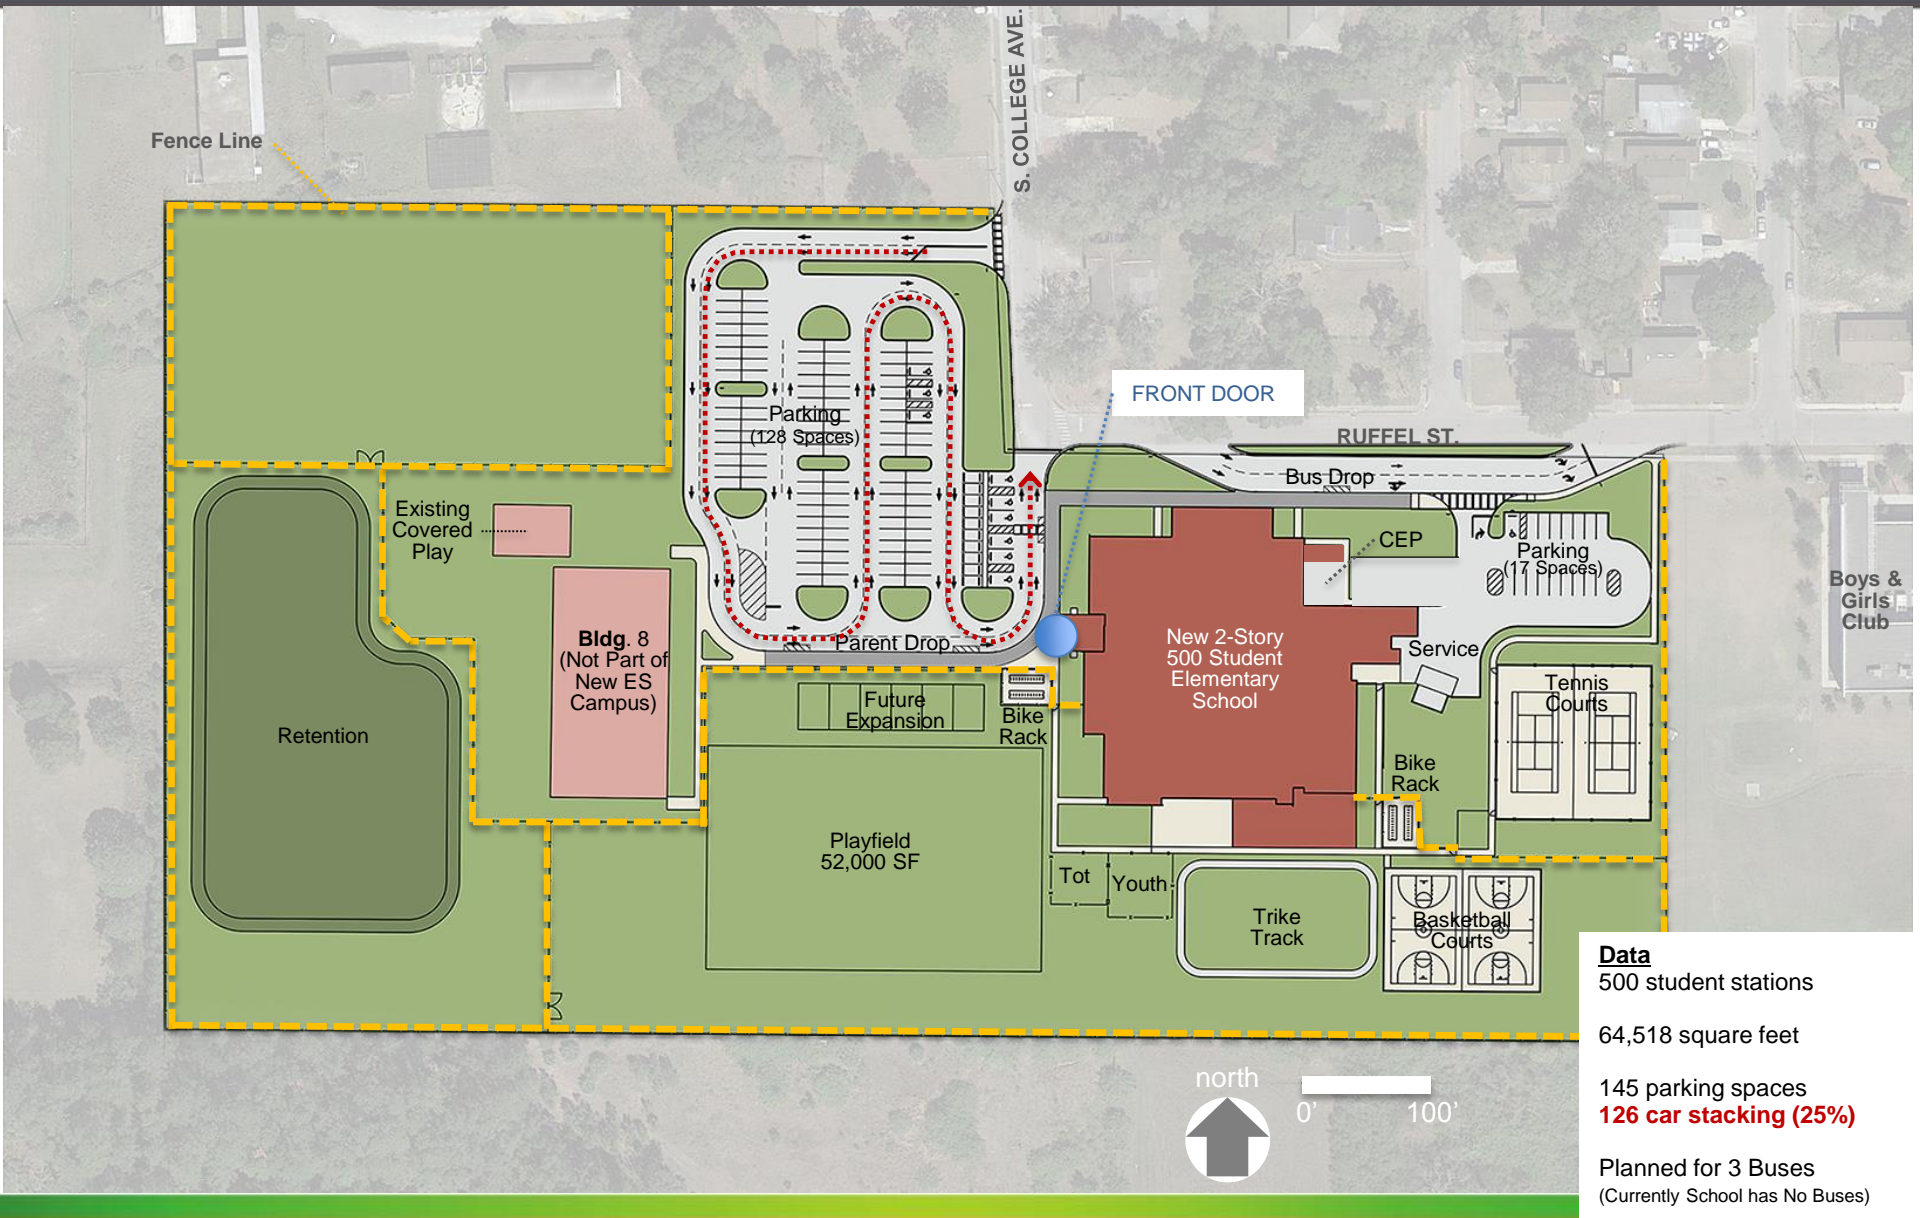

Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Construction Update and Milestones

- Notice to Proceed (NTP) was issued July 27, 2017
- Tilt Wall Panels were completed on November 12, 2017
- Structural Steel Erection was completed on January 4, 2018
- Roofing work has begun and will be completed by February 23, 2018
- Window installation started and will be completed by March 8, 2018
- Exterior painting to begin March 2, 2018
- Interior work is in progress
- Project remains on schedule for Substantial Completion May 17, 2018

Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools





Building Foundations



Underslab Rough In



Slab on Grade Pour



Tilt Panel Rebar



Tilt Panel Erection



Steel Erection



Lightweight Installation



Roofing Installation

Questions and Answers
