

Orange County Public Schools



40% Construction Community Meeting
Meadow Woods Elementary
March 8, 2017

WINNER

the broad prize
for urban education




**Welcome! Please sign in
on your mobile device:**
<http://communitymeeting.ocps.net/>

Meadow Woods Elementary School Meeting Agenda

March 8, 2017 6:00 PM

- Welcome – School Board Member: Linda Kobert
- Introductions – Community Meeting Organizer Lauren Roth
- Project Update – Facilities Meeting Organizer
Architect: **SCHENKELSHULTZ**
ARCHITECTURE
Contractor:  **WELBRO**
BUILDING CORPORATION
- Questions and Answers
- Adjournment

Orange County Public Schools

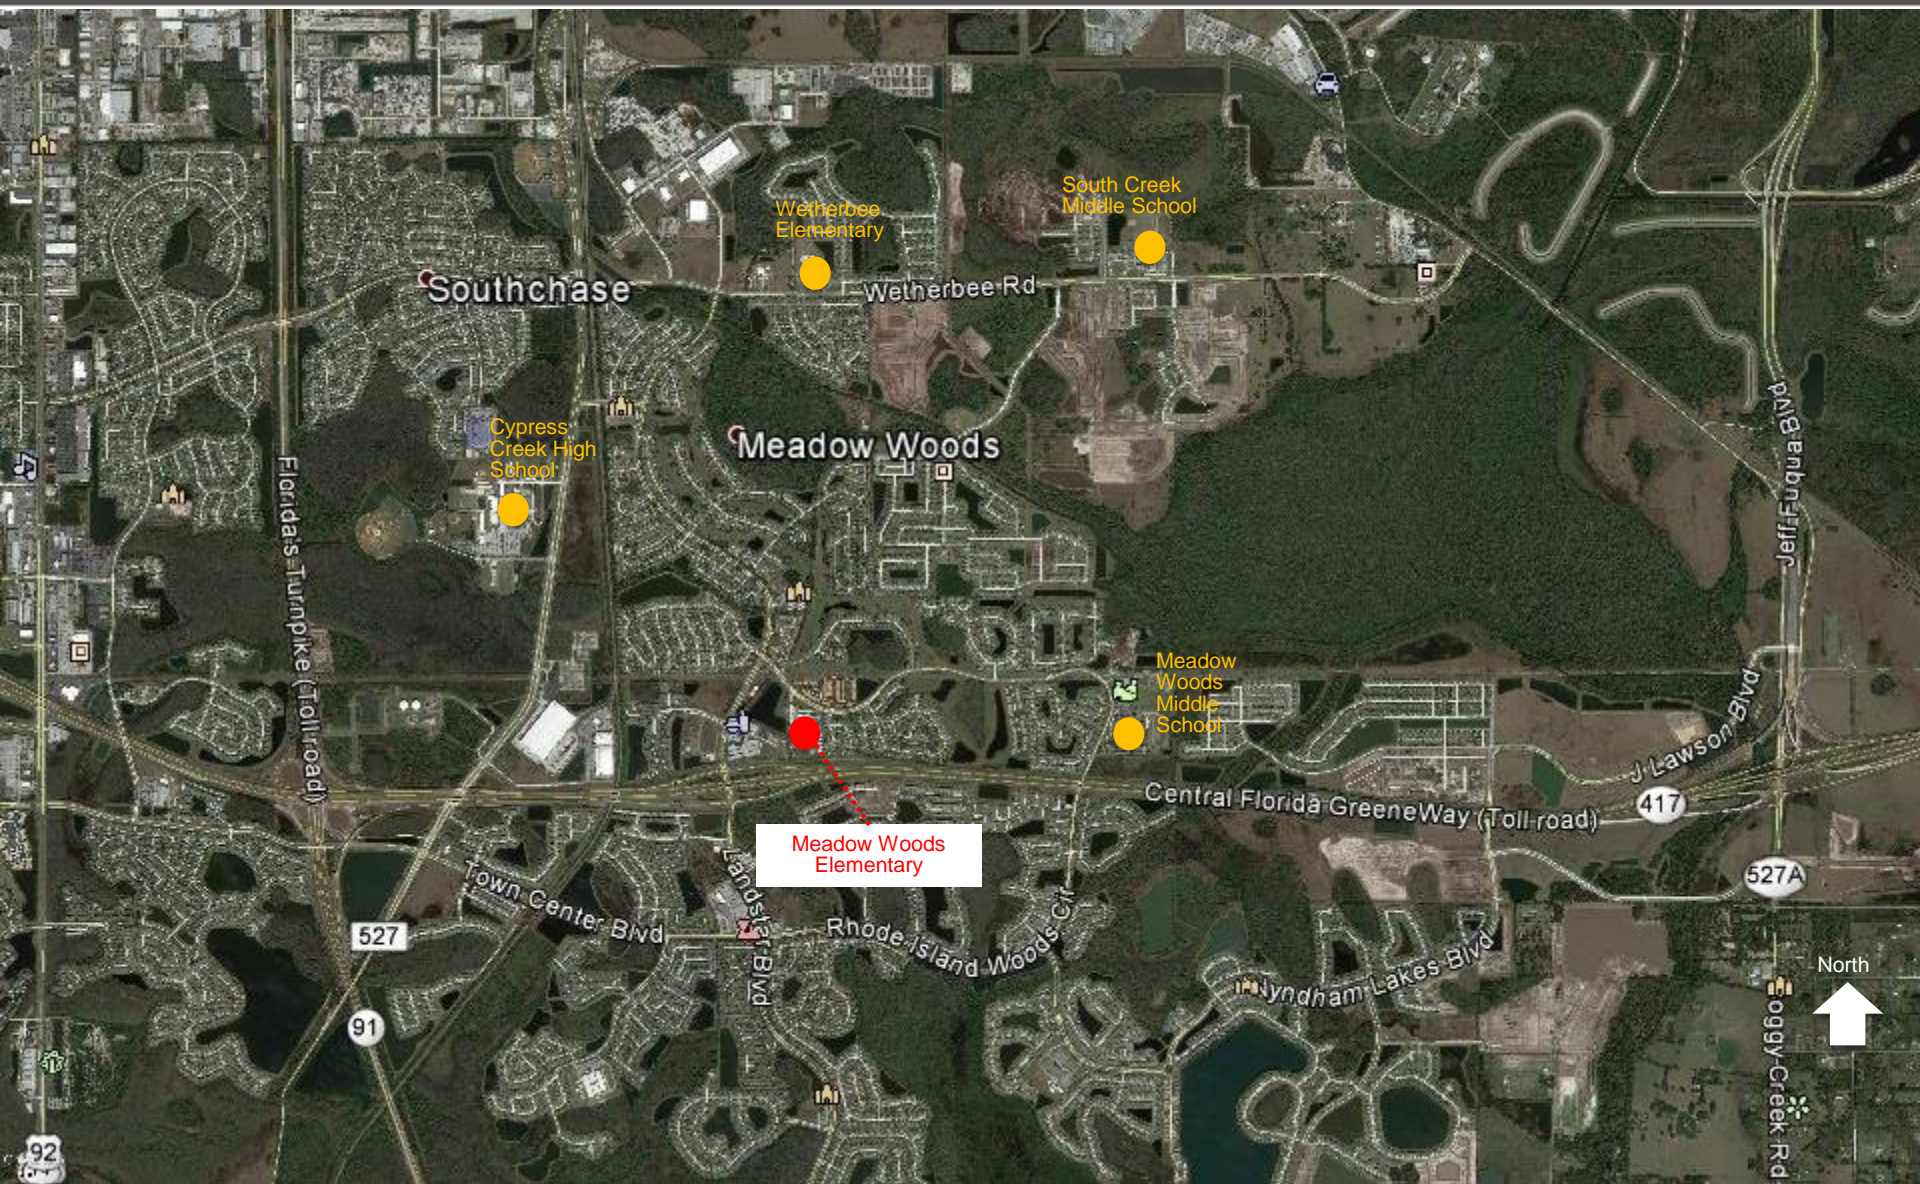


Orange County Public Schools



Orange County Public Schools



Orange County Public Schools

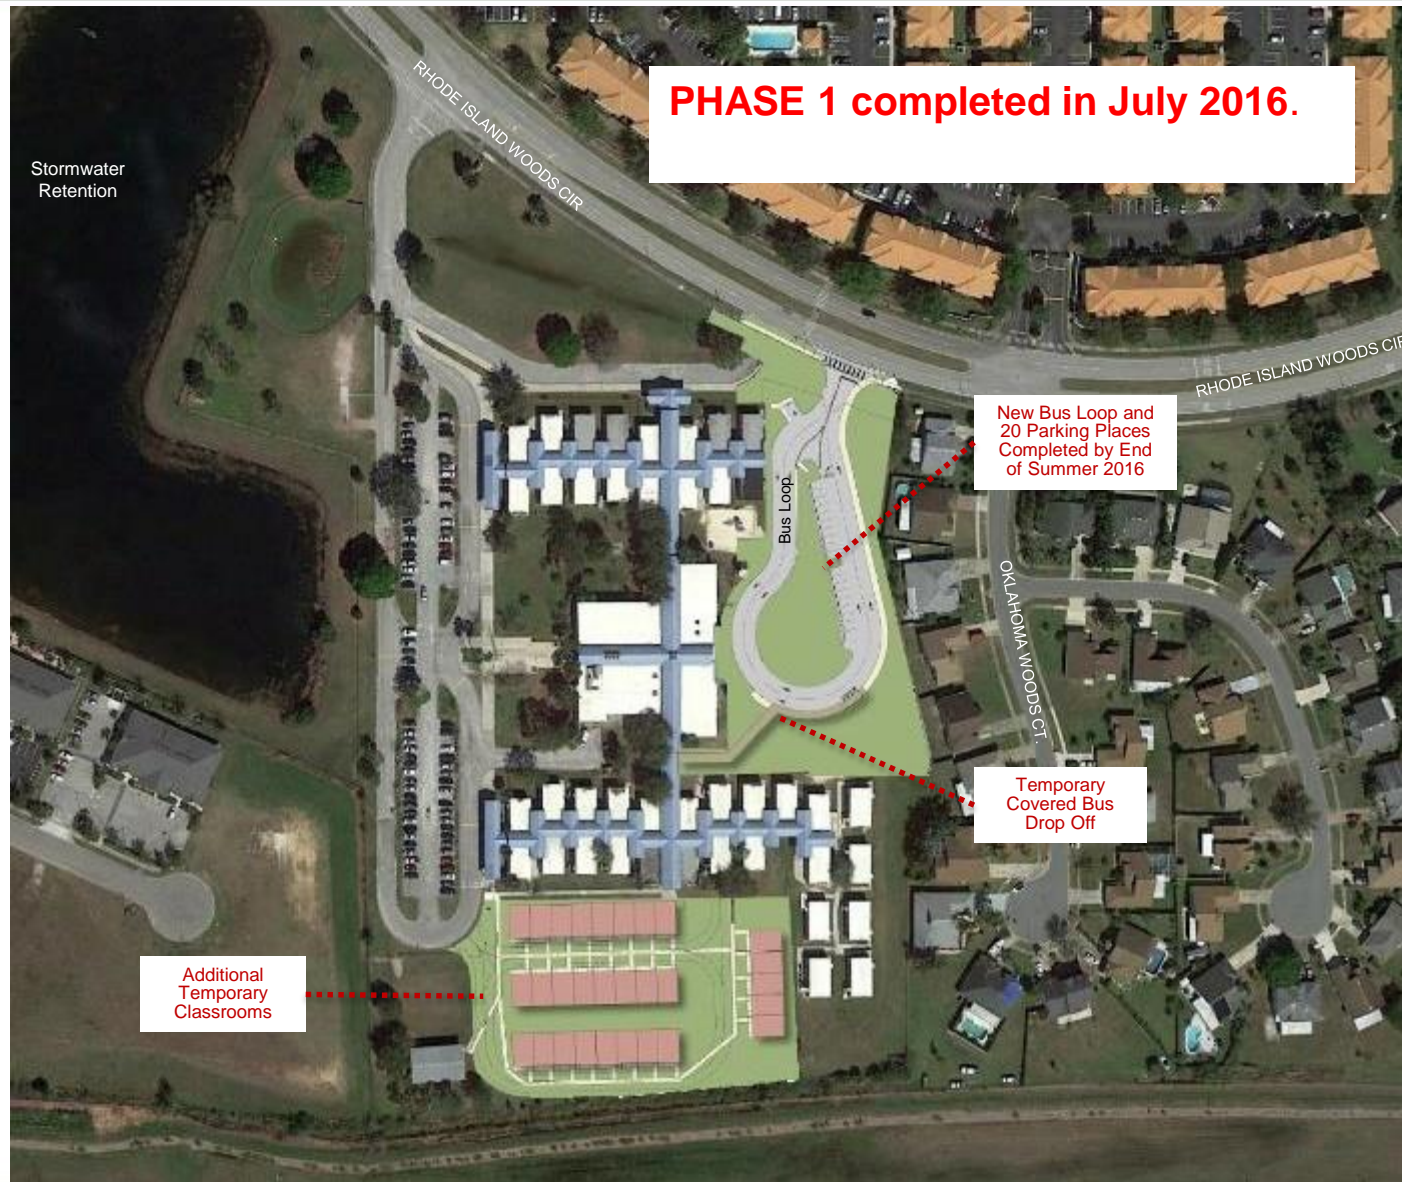

Orange County Public Schools



Orange County Public Schools



Data

837 student stations

90,019 square feet

170 parking spaces

123 car stacking

15 Buses

security cameras

Orange County Public Schools



Orange County Public Schools



Construction Update and Milestones:

- Notice to Proceed (NTP) was July 11, 2016
- Tilt wall panels were completed by December 07, 2016 (two months after NTP)
- Structural Steel Erection started on December 14, 2016 and was completed by January 22, 2017
- Roofing work started on January 08, 2017 and completed on February 24, 2017
- Interior work is in progress with wall framing, MEP rough-in installation and drywall
- Project remains on schedule for Substantial Completion on May 31, 2017 for Phase 2 (Two Story Building).

Orange County Public Schools



Construction Logistics Plan

Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools



Orange County Public Schools




Orange County Public Schools



Orange County Public Schools



Orange County Public Schools

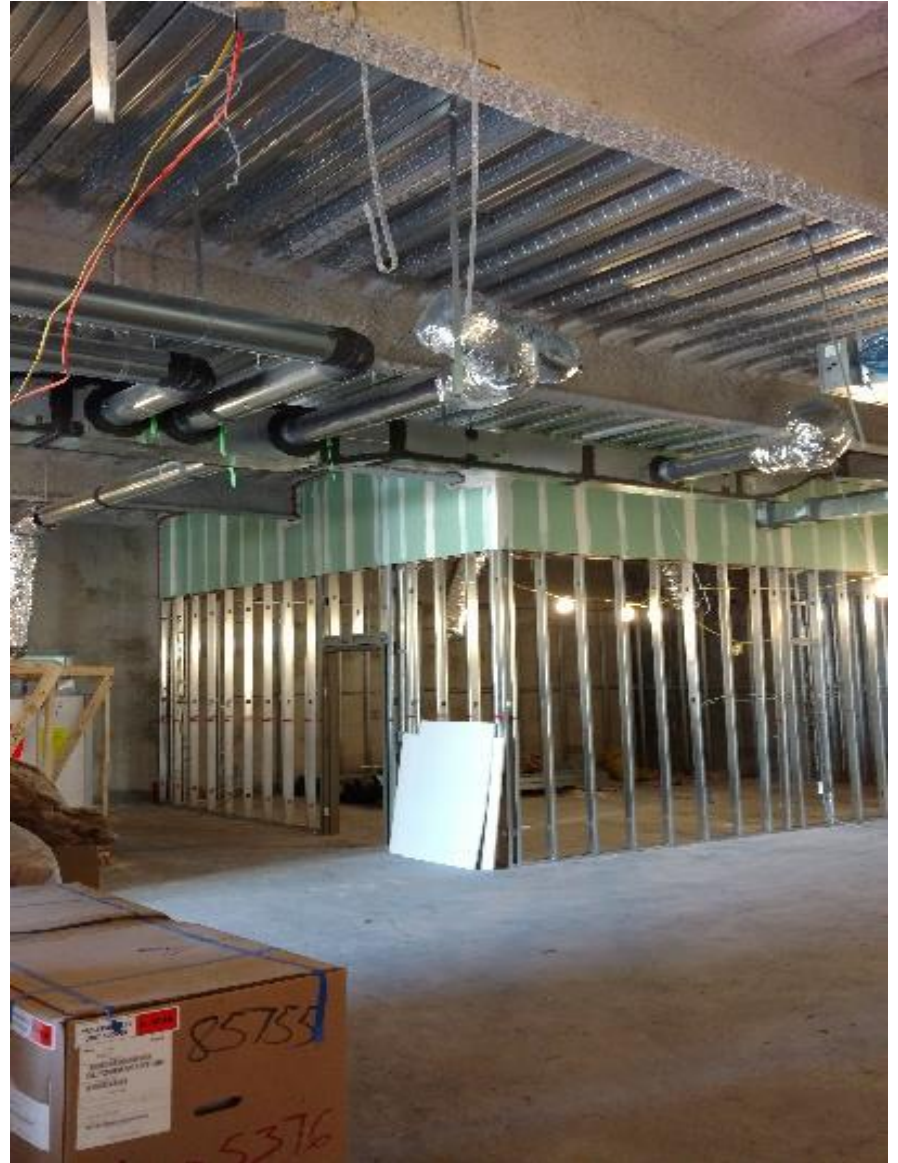

Orange County Public Schools



Orange County Public Schools



Questions and Answers
