


Pine Hills Elementary School

Kathleen "Kat" Gordon School Board Member District 5 Monday, February 26, 2018

# Pine Hills Elementary 40% Construction Update Agenda

February 26, 2018, Robinswood Middle School, 6:00 pm

- Opening Remarks & Introduction of Public Officials Kathleen "Kat" Gordon
- Acknowledgements & Introductions of Project Team Jessma Lambert
- Project Update Architect: BRPH Architects/Engineers, Inc.
   Construction Manager: Pirtle Construction
- Questions and Answers
- Adjournment

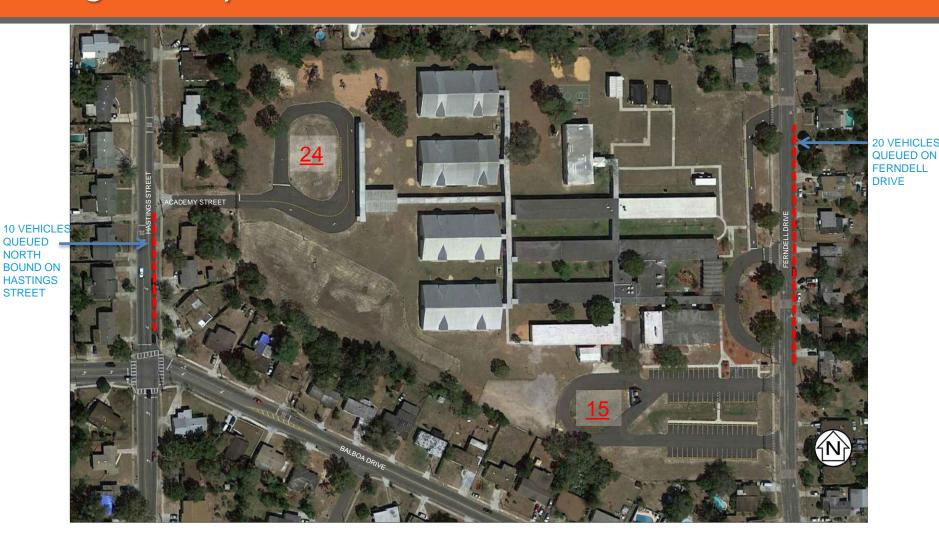

**Existing Counts:** 

**NORTH** 

**STREET** 

Maximum Observed Queuing: 69 Vehicles

**Existing Parking: 73 Vehicles** 





Existing:

Queuing: 69 Cars Parking: 73 Cars

Bus: 1

Required:

Queuing: 82-120 (Max) Cars Parking: 82 (Staff)+10 (Visitor)=92 Bus: 2

Bus: 3

Provided:

Percent Stacking: 19.3% Total Queuing: 162 Cars Total Parking: 128 Cars Student Capacity: 837 1st Floor: 63,121 SF Covered Play: 2,224 SF 2nd Floor: 31,208 SF










South






North



## **Construction Updates and Milestones:**

- Notice to Proceed (NTP) was July 18, 2017.
- Site clearing, grading, and retention pond were completed in October.
- Tilt wall panels were completed in November.
- Structural steel erection was completed in January.
- Roofing work is 70% complete, dry-in complete.
- Window installation complete in January.
- Framing and MEP above ceiling installation has started.
- Project is 50% complete as of February 16, 2018.
- Project on schedule for Substantial Completion on June 30, 2018.

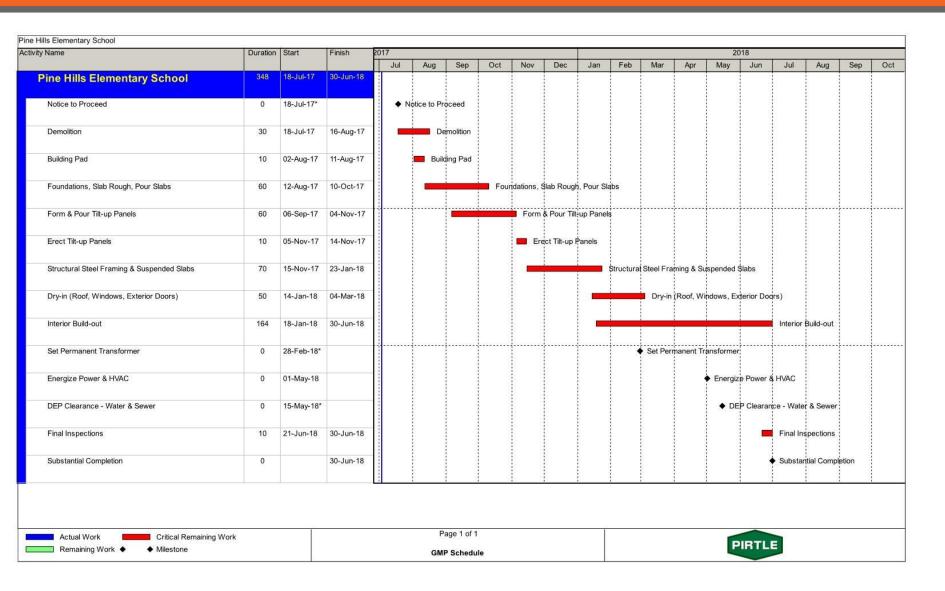





Pine Hills Elementary School Project Number C-0094 09-21-17







Pine Hills Elementary School Project Number C-0094 10-19-17







Pine Hills Elementary School Project Number C-0094 11-20-17







Pine Hills Elementary School Project Number C-0094 12-20-17








Pine Hills Elementary School Project Number C-0094 01-18-18




#### Finishing Tilt Panels and Kitchen Slab

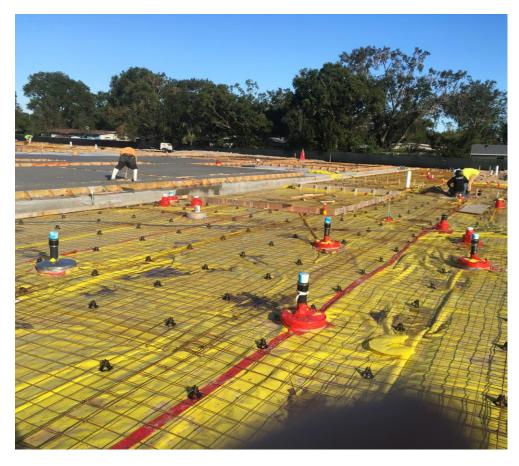



**Pouring Tilt Panels** 

# Erecting of Tilt Panels with 250 Ton Crane

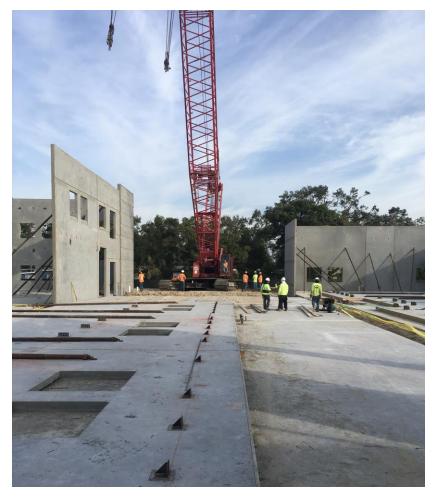



**Erecting Structural Steel** 

#### **Install Roof Deck**





Install LWIC

Form Sidewalk and Canopy Footings





**Paint Building Exterior** 

#### Install Kitchen Tile






Kitchen Hood Install

#### Principal's Office



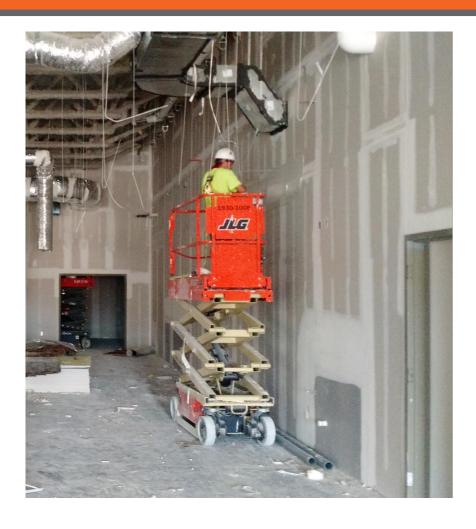

Tape and Finish Dining Room Drywall

## Questions?

Facilities contact person for School Board District 5

Jessma Lambert

Facilities Director, Construction Planning

407-317-3700

Thank you to Orange County taxpayers for the ½ penny sales tax, which makes this construction possible.
