

Orange County Public Schools



Welcome! Please sign in
on your mobile device:
<http://communitymeeting.ocps.net/>



Union Park Elementary School
40% Construction Community Meeting
January 17, 2018

Union Park Elementary School 40% Construction Community Meeting

Meeting Agenda

January 17, 2018, 6:00 PM – Union Park Elementary School

- **Welcome** – Joie Cadle, School Board Member - District 1
- **Introductions** – Lauren Roth, Senior Manager, Facilities Communications
- **Project Update** – Architect: Zyscovich Architects

Construction Manager: Pirtle Construction

- **Questions and Answers**
- **Adjournment**

Orange County Public Schools



Orange County Public Schools



Substantial Completion October 2018


Construction Update and Milestones:

- Notice to Proceed (NTP) was July 27, 2017.
- Site clearing, grading and retention pond were completed in October.
- Tilt wall panels were completed in November .
- Structural Steel Erection was completed in December.
- Roofing work is 30% complete.
- Installation of deep storm drainage is ongoing.
- Framing and Mechanical/Electrical/Plumbing above ceiling installation has started.
- Project is 40% complete.

Schedule

Activity

Duration

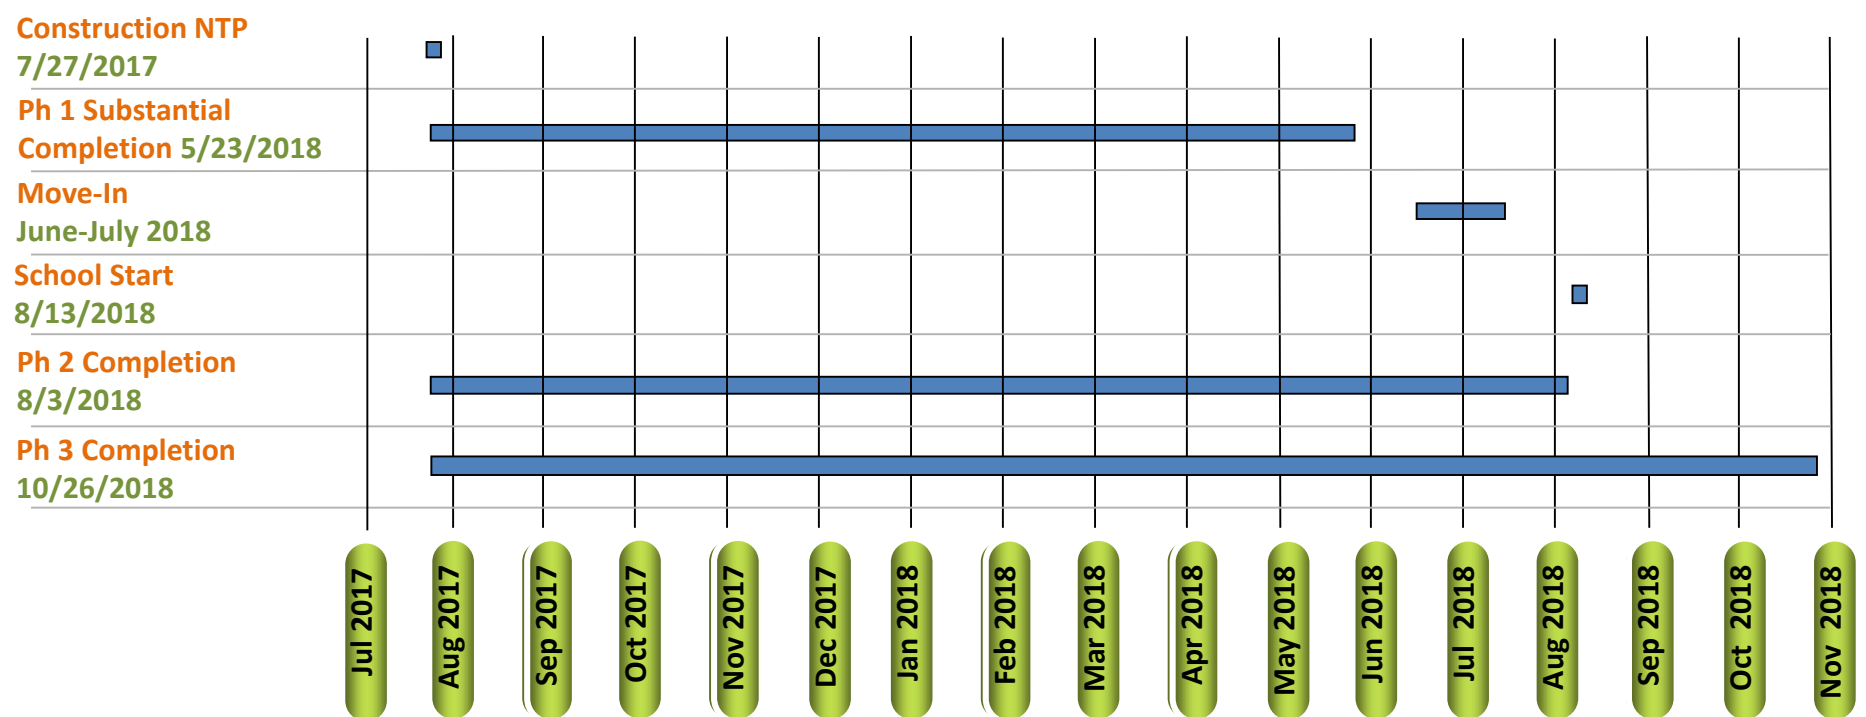



Union Park Elementary School



08-18-17



Union Park Elementary School





Union Park Elementary School



10-20-17



Union Park Elementary School






Union Park Elementary School





Forming of Tilt Panels on Casting Beds

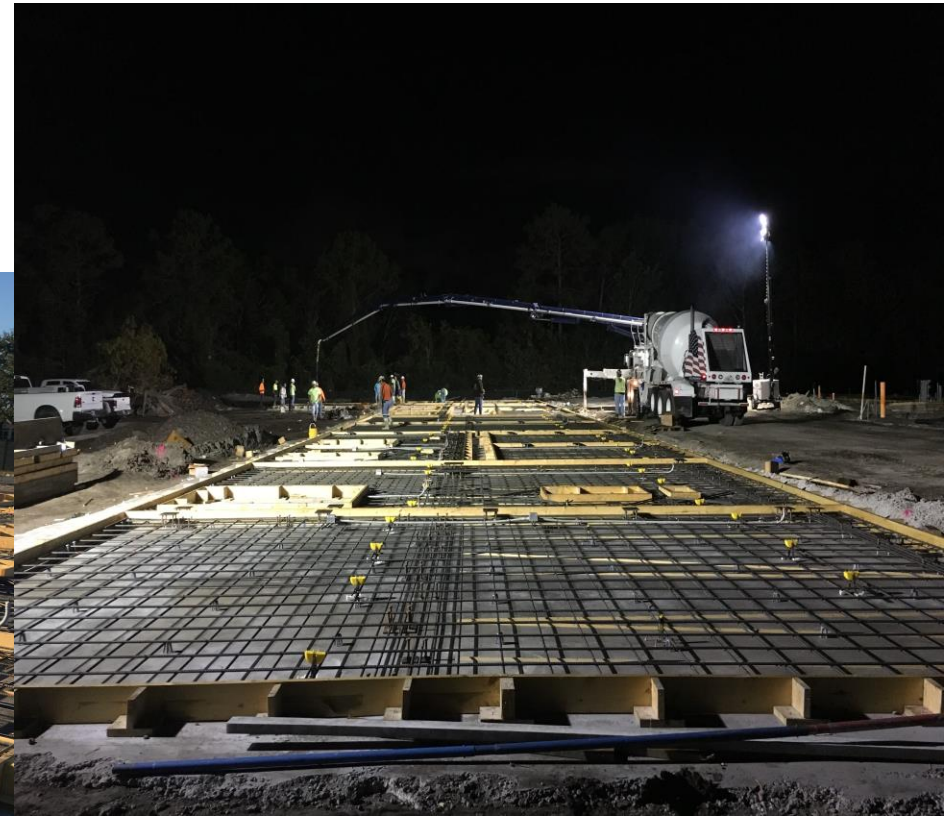


Pouring of Tilt Panels with a Boom Pump

Erection of Tilt Panels with 250 Ton Crawler Crane



Erection of Tilt Panels and Structural Steel

Preparation of Tilt Panels for Structural Steel Installation

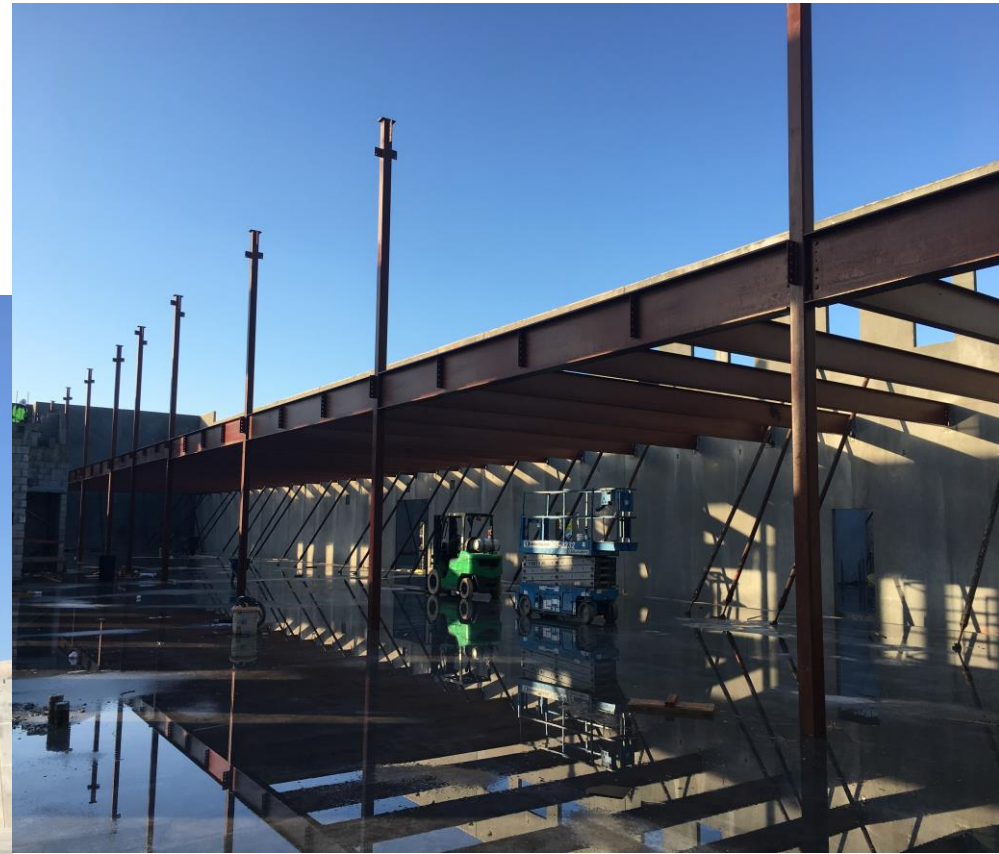

Structural Steel for Second Floor Deck

Installation of Deep Storm Drainage Pipe and Structures



Roof Deck Installation

MEP Hangers and Rough-in
above Ceiling ongoing.



Exterior Grading ongoing

Questions & Answers
