

COVE Meeting

CITIZENS' CONSTRUCTION OVERSIGHT AND VALUE ENGINEERING

September 20, 2023

COVE Meeting Agenda

Wednesday, September 20, 2023 8:00 a.m. – 10:00 a.m.

1. Call to Order and Approval of Meeting Minutes

- Chair Comments Pat Knipe
 - Recognition of Orange Technical College Orlando Campus site visit on August 3, 2023
- Approval of June 15, 2023 Meeting Minutes

2. Review Action Items

- Provide overview of the comprehensive project at Howard MS
- Reconsider Capital Renewal Funding Formula

3. Department Reports

- Capital Funding Update Judith Padres
- Master Schedule Update Basem Ghneim / Mark O'Connor
- Project Budget Update Basem Ghneim / Mark O'Connor
- Project Status Report Craig Jackson
- Change Order Report Ed Ames / Basem Ghneim

4. Presentations

- Howard MS Comprehensive Renovation Project Mo Arthur
- Capital Renewal Funding Formula Basem Ghneim

5. Discussion and Adjournment

- Orange's Half-Penny Sales Tax Scott Howat
- Next COVE meeting scheduled on Thursday, October 19, 2023





The Construction Oversight and Value Engineering Committee monthly meeting convened on Thursday, June 15, 2023 at 8:00 a.m., at the John T. Morris Facilities Complex, located at 6501 Magic Way, building 200, Orlando, Florida 32809, and virtually through Cisco WebEx.

ATTENDEES

COVE Members: Pat Knipe, Jacki Churchill, George Hack, Jeff Hart, Douglas Kelly and Stuart Kramer.

OCPS Team: Faz Ali, Ed Ames, Mary Lu Bronson, Gerard Cattani, Selimar Colon, Doreen Concolino, Catina Cummings, Amy Envall, Mari Espinal, Craig Jackson, Linda Lindsey, Lori Orr, Judith Padres, Tonya Page-Batson, Traci Parks-Chillon, Rory Salimbene, Chris Solomon and Rocco Williams.

Program Management Team: Mo Arthur, Basem Ghneim, Toni Greene, Krista McArthur, Mark O'Connor, Brian Smith and Bill Terry.

1. CALL TO ORDER

A quorum was established and Chairman Pat Knipe called the meeting to order at 8:00 a.m.

Chair Comments

Pat Knipe stated the observation by Jeff Hart for the committee to be involved in the planning process was a good recommendation.

Chair asked Judith Padres to give a brief update on the reconsideration of the Capital Renewal Funding Formula. Rory Salimbene stated this would be a joint activity in determining where to align revenue with our current costs and asked that the topic be rescheduled for a future meeting.

Vice-chair Douglas Kelly questioned whether recent legislative action would impact our school designs. Rory stated he does not foresee legislative actions significantly impacting the cost of schools. Local decisions regarding facilities required to support student needs will have a more significant impact. An example is the desire of our Board to accommodate everyone with safe restroom facilities, in response to HB 1521/SB 1674, Safety in Private Spaces Act.

Approval of Minutes from Last Meeting

The minutes from May 18, 2023 were presented, and approved unanimously by the committee.

2. ACTION ITEMS

- a. Provide an overview of the comprehensive project at Howard Middle School.
- b. Provide analysis and assessment of the adequacy of the Capital Renewal funding formula (tabled from previous meeting).

Review of Action Items from Previous Meeting

a. Provide analysis and assessment of the adequacy of the Capital Renewal funding formula (tabled to an upcoming meeting).

3. DEPARTMENT REPORTS

Capital Funding Update

Judith Padres provided the *capital funding update*, and highlighted the following from the report:

• Sales tax collections are higher than projected and currently at \$304.3M.



- Total sales tax revenue exceeds \$4.2B.
- The capital renewal balance is currently \$684.1M.

Judith highlighted the following regarding impact fees:

- Current collections total \$70M.
- Impact fees include three payments from the County and 10 payments from the City of Orlando.

When asked regarding CIT (capital improvement tax) revenues, Judith explained that we annually place a newspaper ad which, based on our property valuation, details how much we expect to collect and how it will be spent (e.g. buses, debt service, safety, security enhancements, white fleet, portable replacement and other expenditures not qualifying for sales tax or impact fees).

- Three funding sources will be used for site 50-H-SE-2 to include Sales Tax, Capital Improvement Tax, and Impact Fees.
- The Capital Improvement Tax (CIT) currently has a fund balance of \$430M, of which \$130M will be used for two new schools.

Also, Judith shared there was a new bill passed this year where we have to share a portion of our revenue with charter schools. This has a five year phase-in that increases annually and may divert up to \$30M from our 1.5 mil revenue (ref. HB 1259/SB 1328, Charter School Capital Outlay Funding).

Master Schedule Update

Mark O'Connor briefed the committee on the *master schedule* on page 20, and highlighted the following:

- A notice to proceed was recently issued on the Howard Middle School Comprehensive Project, and the project has moved into construction.
- Orange Center Parking Garage repurpose project was recently placed on hold pending sufficient enrollment to support the need.
- > Pat Knipe questioned if capacity enhancement projects are synonymous with functional equity.

Rory Salimbene explained capacity enhancement is a new term that replaces a portion of what was previously called functional equity, and focuses on the additional capacity needed to satisfy projected enrollment at existing schools that cannot be satisfied by a new relief school.

Rory added that functional equity is a separate category focused on missing program elements that are included in our current prototypes. An example of a functional equity requirement is a gymnasium at a middle school which currently has none.

In addition to site 130-E-SE-2, Jeff Hart questioned if there were plans for site 97-E-SE-2, or if it was on hold.

Rory stated that although there were real estate challenges for this site, milestones leading to a 2025 opening would be added for the next meeting.

> Jeff Hart asked whether there were further updates on the OTC South campus.

Rory confirmed this project was on hold while the program was finalized but expected the needed decisions soon that would allow the design phase to commence.

Project Budget Update

Mark O' Connor continued with his review of the *capital project report* on page 23, highlighting the following:

• The new and replacement schools in the report encompass 10 projects amounting to \$656M.



> Jeff Hart pointed out the absence of replacement projects within the planning phase.

Mark confirmed we have completed the list of 136 school projects, excluding the OTC South campus, and that no complete replacements were planned for the current group of comprehensive projects.

Jeff Hart inquired about the Group 3 schools, and whether there was any level of replacement or partial replacement for these schools.

Mark stated those projects would be comprehensive renovations.

Next, Mark noted there were no budget changes on the 25 comprehensive projects, which amount to \$927M.

Continuing with *capital renewal*, Mark highlighted two added projects: Audio Enhancement Intercom Pilot for \$1.4M and Dr. Phillips North Premise Wiring for \$75K.

> Jeff Hart questioned if the scope for the Audio Enhancement project included more than one campus.

Basem stated the project included an elementary, a middle and a high school campus.

Lastly, Mark reviewed the capital renewal forecast on page 29, noting there is a fund balance of \$684.1M.

Project Status Report

Craig Jackson reviewed the *capital and comprehensive needs* projects currently under construction, noting the following:

- OTC Orlando received a temporary certificate of occupancy (TCO), and has moved into phase 2 on the other side of the building.
- At Hungerford Building 8, roof purlins have now been placed.
- Water Spring Middle School is slightly behind schedule due to delays on items with the hurricane rating of the gymnasium building, with completion expected by the end of June.
- New high school site 50-H-SE-2 in the Lake Nona area is progressing on schedule.
- Site 73-T-W-7 replacement project continues and is scheduled for completion in February 2024, although an anticipated time extension may result in a mid-March 2024 completion.
- > Pat Knipe asked if we have been delayed by delivery timelines for materials or a shortage of labor.

Craig stated we have not experienced significant delays and are using separate GMP packages for early ordering of equipment to mitigate the impact.

> George Hack asked if we continue to test the permeability of soils on sites.

Craig confirmed they continue to be tested.

Craig ended his report by stating there are 52 active *capital renewal projects* in planning, design and construction at 109 sites, and noted the following:

- There are currently 21 projects in construction at 50 sites (10 large, five intermediate and six small).
- The Thornebrooke Elementary School project scope includes an upgrade of the building automation system (BAS) for the whole campus that will be completed over the summer.
- > Jeff Hart questioned what Maintenance can do to support longevity of the equipment.

Rory indicated that there were many capital renewal projects addressing maintenance intensive and aging systems with more maintenance-friendly designs (e.g. replacement of fan terminal boxes with a



variable air volume box that has no fans) that once completed would reduce maintenance requirements and allow the Maintenance staff to increase focus on preventive measures.

Change Order Report

Ed Ames reported the data for the month of May 2023, and stated there were no significant change orders for the reporting period.

For page 49, item 4, Jeff Hart questioned the reduction to general conditions for the new high school in the amount of (\$667,788.70) and if there was an opposing change order for the same value for GMP 1.

Ed confirmed one was presented at Doc Review this past week and will be on next month's report. Rory added that the increase needs board approval.

Ed concluded his report and stated there were no new RFQs for this month's report.

4. PRESENTATIONS

None

5. DISCUSSION / ADJOURNMENT

Pat Knipe asked the committee if there was a need for the July 20, 2023 meeting. A motion to cancel the meeting was presented, and was approved unanimously by the committee.

In addition, the meeting scheduled for August was discussed, as it historically has been used as a site visit to one of the new schools. One suggestion was to visit Howard Middle School, and due to the lack of construction progress, a motion to visit the Orange Technical College Orlando Campus on August 3, 2023 at 9:00 AM was presented, and approved unanimously.

Jeff Hart requested that staff provide an overview of the Howard Middle School Comprehensive Project at an upcoming meeting, adding that COVE should have an understanding of how the funding is spent and why.

The meeting was adjourned at 9:12 a.m.

Minutes Authenticated by:

Pat Knipe Chairperson, COVE Committee Date of approval

Jad Brewer Legal Services, Facilities Date of approval

Attachments: None

CAPITAL FUNDING UPDATE

FY2024 Sales Tax Forecast Compared To Collections For Collections Received For The Period June 1, 2023 - May 31, 2024

| Fiscal Year | Fiscal Year | Fiscal Year | Fiscal Year | Fiscal Year
 | Fiscal Year
 | Fiscal Year |
 | |
 | | |
 | | | |
|-----------------------|---|--|--
--
--|---|---
--
---|---

--|--|---|---
---|---|
| 2019 | 2020 | 2021 | 2022 | 2023
 | 2024
 | 2024 |
 | |
 | | |
 | | | |
| Actual
Collections | Actual
Collections | Actual
Collections | Actual
Collections | Actual
Collections
 | Projected
Collections
 | Actual
Collections | Date
Received
 | Difference
Monthly | % Difference
Monthly
 | Difference
Year To Date | |
 | | | % Cum Difference
With Prior Year |
| 21,813,615 | 22,925,741 | 13,108,514 | 23,848,325 | 28,818,745
 | 24,933,405
 | 28,368,958 | 8/28/2023
 | 3,435,553 | 13.78%
 | 3,435,553 | 13.78% | (449,787)
 | -1.56% | (449,787) | -1.56% |
| 20,771,709 | 21,966,783 | 13,655,914 | 23,820,627 | 26,552,569
 | 24,271,373
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 19,375,685 | 20,607,144 | 13,689,148 | 20,150,373 | 25,312,864
 | 22,422,764
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 3,260,952 | 3,338,214 | 4,014,607 | 5,620,309 | 7,333,106
 | 6,432,030
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 65,221,961 | 68,837,881 | 44,468,184 | 73,439,633 | 88,017,283
 | 78,059,572
 | 28,368,958 |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| 20.029.499 | 20.695.054 | 15.713.676 | 21.896.095 | 25.711.154
 | 24.002.925
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 21,176,213 | 22,650,187 | 15,709,696 | 23,905,773 | 27,564,584
 | 25,465,794
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 21,848,770 | 23,121,776 | 16,337,370 | 25,794,011 | 27,841,619
 | 26,524,510
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 3,646,732 | 3,532,907 | 4,523,961 | 7,274,990 | 7,902,837
 | 7,468,313
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 66,701,214 | 69,999,923 | 52,284,704 | 78,870,869 | 89,020,194
 | 83,461,542
 | - |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| 131,923,175 | 138,837,805 | 96,752,888 | 152,310,502 | 177,037,477
 | 161,521,114
 | 28,368,958 |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| 23 379 047 | 25 393 825 | 17 165 676 | 28 708 776 | 32 031 954
 | 29 531 809
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| , , | | | | , ,
 | , ,
 | |
 | 0 |
 | - | | 0
 | | - | 0.00% |
| , , | , , | , , | , , | , ,
 | , ,
 | |
 | 0 |
 | - | | 0
 | | - | 0.00% |
| , , | , , | , , | |
 | , ,
 | |
 | 0 |
 | - | | 0
 | | - | 0.00% |
| 69,412,273 | 74,438,972 | 55,257,984 | 85,992,429 | 95,412,488
 | 89,711,282
 | - |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| 201.335.448 | 213.276.777 | 152.010.872 | 238.302.930 | 272.449.966
 | 251,232,396
 | 28.368.958 |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| | -, -, | - ,,- | | , ,,,,,,,
 |
 | -,, |
 | |
 | | |
 | | | |
| 25,501,978 | 16,298,832 | 23,660,893 | 31,317,507 | 31,873,069
 | 32,922,594
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 22,737,566 | 9,524,264 | 21,512,382 | 28,431,166 | 29,167,856
 | 29,988,585
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 21,730,575 | 11,135,296 | 21,709,815 | 27,010,484 | 27,202,256
 | 28,779,795
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 3,151,332 | 3,730,011 | 4,753,904 | 7,350,019 | 7,597,320
 | 7,468,106
 | |
 | 0 | 0.00%
 | - | 0.00% | 0
 | 0.00% | - | 0.00% |
| 73,121,451 | 40,688,403 | 71,636,994 | 94,109,175 | 95,840,501
 | 99,159,080
 | - |
 | |
 | - | 0.00% |
 | | - | 0.00% |
| 142,533,724 | 115,127,375 | 126,894,978 | 180,101,604 | 191,252,989
 | 188,870,362
 | - |
 | |
 | - | 0.00% |
 | | | 0.00% |
| 274,456,899 | 253,965,180 | 223,647,866 | 332,412,105 | 368,290,467
 | 350,391,476
 | 28,368,958 |
 | |
 | - | 0.00% | | | | | | | | | | | | | | |
 | | - | 0.00% |
| | 2019
Actual
Collections
21,813,615
20,771,709
19,375,685
3,260,952
65,221,961
20,029,499
21,176,213
21,848,770
3,646,732
66,701,214
131,923,175
23,379,047
21,073,611
21,507,567
3,452,049
69,412,273
201,335,448
25,501,978
22,737,566
21,730,575
3,151,332
73,121,451
142,533,724 | 2019 2020 Actual
Collections Actual
Collections 21,813,615 22,925,741 20,771,709 21,966,783 19,375,685 20,607,144 3,260,952 3,338,214 65,221,961 68,837,881 20,029,499 20,695,054 21,176,213 22,650,187 21,848,770 23,121,776 3,646,732 3,532,907 66,701,214 69,999,923 131,923,175 138,837,805 23,379,047 25,393,825 21,073,611 23,118,851 21,507,567 21,922,091 3,452,049 4,004,206 69,412,273 74,438,972 201,335,448 213,276,777 25,501,978 16,298,832 22,737,566 9,524,264 21,730,575 11,135,296 3,151,332 3,730,011 73,121,451 40,688,403 142,533,724 115,127,375 | 2019 2020 2021 Actual
Collections Actual
Collections Actual
Collections 21,813,615 22,925,741 13,108,514 20,771,709 21,966,783 13,655,914 19,375,685 20,607,144 13,689,148 3,260,952 3,338,214 4,014,607 65,221,961 68,837,881 44,468,184 20,029,499 20,695,054 15,713,676 21,176,213 22,650,187 15,709,696 21,848,770 23,121,776 16,337,370 3,646,732 3,532,907 4,523,961 66,701,214 69,999,923 52,284,704 131,923,175 138,837,805 96,752,888 23,379,047 25,393,825 17,165,676 21,507,567 21,922,091 17,365,549 3,452,049 4,004,206 4,909,457 69,412,273 74,438,972 55,257,984 201,335,448 213,276,777 152,010,872 25,501,978 16,298,832 23,660,893 22,737,566 9,524,264 21,512,38 | 2019 2020 2021 2022 Actual
Collections Actual
Collections 2022 Actual
Collections 21,813,615 22,925,741 13,108,514 23,848,325 20,771,709 21,966,783 13,655,914 23,820,627 19,375,685 20,607,144 13,689,148 20,150,373 3,260,952 3,338,214 4,014,607 5,620,309 65,221,961 68,837,881 44,468,184 73,439,633 20,029,499 20,695,054 15,713,676 21,896,095 21,176,213 22,650,187 15,709,696 23,905,773 21,848,770 23,121,776 16,337,370 25,794,011 3,646,732 3,532,907 4,523,961 7,274,990 66,701,214 69,999,923 52,284,704 78,870,869 131,923,175 138,837,805 96,752,888 152,310,502 23,379,047 25,393,825 17,165,676 28,708,776 21,073,611 23,118,851 15,817,302 23,523,330 21,507,567 21,922,091 17,365,549 <td>2019
Actual
Collections 2020
Actual
Collections 2021
Actual
Collections 2022
Actual
Collections 2023
Actual
Collections 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 20,771,709 21,966,783 13,655,914 23,820,627 26,552,569 19,375,685 20,607,144 13,869,148 20,150,373 25,312,864 3,260,952 3,338,214 4,014,607 5,620,309 7,333,106 65,221,961 68,837,881 44,468,184 73,439,633 88,017,283 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 21,176,213 22,650,187 15,709,696 23,905,773 27,64,584 21,848,770 23,121,776 16,337,370 25,794,011 27,841,619 3,646,732 3,532,907 4,523,961 7,274,990 7,902,837 66,701,214 69,999,923 52,284,704 78,870,869 89,020,194 131,923,175 138,837,805 96,752,888 152,310,502 177,037,477 23,379,047 25,393,825 1</td> <td>2019 2020 2021 2022 2023 2024 Actual
Collections Actual
Collections 2021 2022 2023 2024 Actual
Collections Collections Collections Collections Collections Collections 21,813.615 22,925,741 13,108,514 23,848,325 26,652,569 24,271,373 20,777,709 21,966,783 13,655,914 23,820,627 26,552,569 24,271,373 3,260,952 3,338,214 4,014,607 5,620,309 7,333,106 6,432,030 65,221,961 68,837,881 44,468,184 73,439,633 88,017,283 78,059,572 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 21,176,213 22,650,187 15,709,696 23,905,773 27,564,584 25,645,574 21,848,770 23,121,776 16,337,370 25,794,011 27,844,1619 26,524,510 3,646,732 3,532,907 4,523,961 7,274,990 7,902,837 7,468,313 66,701,2</td> <td>2019
Actual
Collections 2020
Actual
Collections 2021
Actual
Collections 2022
Actual
Collections 2023
Actual
Collections 2024
Actual
Collections 21,813,615 22,925,741 13,108,514 23,820,627 26,525,569 24,271,373 28,368,958 20,059,52 3,332,214 4,014,607 5,620,309 7,331,08 6,432,030 6,432,030 21,176,213 22,650,187 15,713,676 21,896,095 25,711,154 24,002,925 21,716,213 22,650,187 7,468,313 66,701,214 69,999,923 52,284,704 78,870,869 89,020,194 83,461,542 - 131,923,175 138,837,805 96,752,888 152,310,502<td>2019 2020 2021 2022 2023 2024 2024 Actual
Collections Date
Collections 2019 Collections Collections</td><td>2019 2020 2021 2022 2023 2024 2024 2024 Difference Actual
Collections Actual
Collections Actual
Collections Actual
Collections Projected
Collections Actual
Collections Date
Collections Difference
Received 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 20,0771,709 21,966,783 13,689,148 20,150,373 25,312,864 22,422,764 0 3,360,952 3,338,214 44,468,184 73,439,633 88,017,283 78,059,572 28,368,958 0 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 21,484,772 23,121,776 16,337,370 25,794,011 27,841,619 25,524,510 0 21,484,772 3,532,907 4,523,961 7,27,990 7,902,837 7,468,313 0 23,379,047 25,338,825 17,165,676 28,708,776 32,031,954 29,531,809<!--</td--><td>2019 2020 2021 2022 2023 2024 2024 2024 Collections Actual
Collections Date
Collections Date
Received Date
Monthly 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 13.78% 19,375,685 20,607,144 13,808,148 23,820,687 25,312,644 24,922,764 0 0.00% 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 0.00% 21,1762,13 22,66187 15,337,370 25,390,777 27,64,642 26,46,574 0 0 0.00% 3,646,732 3,532,907 4,523,961</td><td>2019 2020 2021 2022 2023 2024 2024 2024 Actual Actual Actual Actual Collections Collection</td><td>2019 2020 2021 2022 2023 2024 <th< td=""><td>2019 2020 2021 2022 2023 2024 2024 Collections Received Received</td><td>2019 2020 2021 2022 2023 2024 2024 Actual
Actual
Actual
Collections Actual
Actual
Collections Actual
Collections Collections 2024 2024 Actual
Actual
Actual
Collections Actual
Collections Collections 2024 Actual
Actual
Actual
Collections Actual
Collections Collections <thcolections< th=""> Collections</thcolections<></td><td>2019 2020 2021 2022 2023 2024 2024 Date Actual VErogettion Actual VErogettion Vert To Date Vert</td></th<></td></td></td> | 2019
Actual
Collections 2020
Actual
Collections 2021
Actual
Collections 2022
Actual
Collections 2023
Actual
Collections 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 20,771,709 21,966,783 13,655,914 23,820,627 26,552,569 19,375,685 20,607,144 13,869,148 20,150,373 25,312,864 3,260,952 3,338,214 4,014,607 5,620,309 7,333,106 65,221,961 68,837,881 44,468,184 73,439,633 88,017,283 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 21,176,213 22,650,187 15,709,696 23,905,773 27,64,584 21,848,770 23,121,776 16,337,370 25,794,011 27,841,619 3,646,732 3,532,907 4,523,961 7,274,990 7,902,837 66,701,214 69,999,923 52,284,704 78,870,869 89,020,194 131,923,175 138,837,805 96,752,888 152,310,502 177,037,477 23,379,047 25,393,825 1 | 2019 2020 2021 2022 2023 2024 Actual
Collections Actual
Collections 2021 2022 2023 2024 Actual
Collections Collections Collections Collections Collections Collections 21,813.615 22,925,741 13,108,514 23,848,325 26,652,569 24,271,373 20,777,709 21,966,783 13,655,914 23,820,627 26,552,569 24,271,373 3,260,952 3,338,214 4,014,607 5,620,309 7,333,106 6,432,030 65,221,961 68,837,881 44,468,184 73,439,633 88,017,283 78,059,572 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 21,176,213 22,650,187 15,709,696 23,905,773 27,564,584 25,645,574 21,848,770 23,121,776 16,337,370 25,794,011 27,844,1619 26,524,510 3,646,732 3,532,907 4,523,961 7,274,990 7,902,837 7,468,313 66,701,2 | 2019
Actual
Collections 2020
Actual
Collections 2021
Actual
Collections 2022
Actual
Collections 2023
Actual
Collections 2024
Actual
Collections 21,813,615 22,925,741 13,108,514 23,820,627 26,525,569 24,271,373 28,368,958 20,059,52 3,332,214 4,014,607 5,620,309 7,331,08 6,432,030 6,432,030 21,176,213 22,650,187 15,713,676 21,896,095 25,711,154 24,002,925 21,716,213 22,650,187 7,468,313 66,701,214 69,999,923 52,284,704 78,870,869 89,020,194 83,461,542 - 131,923,175 138,837,805 96,752,888 152,310,502 <td>2019 2020 2021 2022 2023 2024 2024 Actual
Collections Date
Collections 2019 Collections Collections</td> <td>2019 2020 2021 2022 2023 2024 2024 2024 Difference Actual
Collections Actual
Collections Actual
Collections Actual
Collections Projected
Collections Actual
Collections Date
Collections Difference
Received 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 20,0771,709 21,966,783 13,689,148 20,150,373 25,312,864 22,422,764 0 3,360,952 3,338,214 44,468,184 73,439,633 88,017,283 78,059,572 28,368,958 0 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 21,484,772 23,121,776 16,337,370 25,794,011 27,841,619 25,524,510 0 21,484,772 3,532,907 4,523,961 7,27,990 7,902,837 7,468,313 0 23,379,047 25,338,825 17,165,676 28,708,776 32,031,954 29,531,809<!--</td--><td>2019 2020 2021 2022 2023 2024 2024 2024 Collections Actual
Collections Date
Collections Date
Received Date
Monthly 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 13.78% 19,375,685 20,607,144 13,808,148 23,820,687 25,312,644 24,922,764 0 0.00% 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 0.00% 21,1762,13 22,66187 15,337,370 25,390,777 27,64,642 26,46,574 0 0 0.00% 3,646,732 3,532,907 4,523,961</td><td>2019 2020 2021 2022 2023 2024 2024 2024 Actual Actual Actual Actual Collections Collection</td><td>2019 2020 2021 2022 2023 2024 <th< td=""><td>2019 2020 2021 2022 2023 2024 2024 Collections Received Received</td><td>2019 2020 2021 2022 2023 2024 2024 Actual
Actual
Actual
Collections Actual
Actual
Collections Actual
Collections Collections 2024 2024 Actual
Actual
Actual
Collections Actual
Collections Collections 2024 Actual
Actual
Actual
Collections Actual
Collections Collections <thcolections< th=""> Collections</thcolections<></td><td>2019 2020 2021 2022 2023 2024 2024 Date Actual VErogettion Actual VErogettion Vert To Date Vert</td></th<></td></td> | 2019 2020 2021 2022 2023 2024 2024 Actual
Collections Date
Collections 2019 Collections Collections | 2019 2020 2021 2022 2023 2024 2024 2024 Difference Actual
Collections Actual
Collections Actual
Collections Actual
Collections Projected
Collections Actual
Collections Date
Collections Difference
Received 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 20,0771,709 21,966,783 13,689,148 20,150,373 25,312,864 22,422,764 0 3,360,952 3,338,214 44,468,184 73,439,633 88,017,283 78,059,572 28,368,958 0 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 21,484,772 23,121,776 16,337,370 25,794,011 27,841,619 25,524,510 0 21,484,772 3,532,907 4,523,961 7,27,990 7,902,837 7,468,313 0 23,379,047 25,338,825 17,165,676 28,708,776 32,031,954 29,531,809 </td <td>2019 2020 2021 2022 2023 2024 2024 2024 Collections Actual
Collections Date
Collections Date
Received Date
Monthly 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 13.78% 19,375,685 20,607,144 13,808,148 23,820,687 25,312,644 24,922,764 0 0.00% 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 0.00% 21,1762,13 22,66187 15,337,370 25,390,777 27,64,642 26,46,574 0 0 0.00% 3,646,732 3,532,907 4,523,961</td> <td>2019 2020 2021 2022 2023 2024 2024 2024 Actual Actual Actual Actual Collections Collection</td> <td>2019 2020 2021 2022 2023 2024 <th< td=""><td>2019 2020 2021 2022 2023 2024 2024 Collections Received Received</td><td>2019 2020 2021 2022 2023 2024 2024 Actual
Actual
Actual
Collections Actual
Actual
Collections Actual
Collections Collections 2024 2024 Actual
Actual
Actual
Collections Actual
Collections Collections 2024 Actual
Actual
Actual
Collections Actual
Collections Collections <thcolections< th=""> Collections</thcolections<></td><td>2019 2020 2021 2022 2023 2024 2024 Date Actual VErogettion Actual VErogettion Vert To Date Vert</td></th<></td> | 2019 2020 2021 2022 2023 2024 2024 2024 Collections Actual
Collections Date
Collections Date
Received Date
Monthly 21,813,615 22,925,741 13,108,514 23,848,325 28,818,745 24,933,405 28,368,958 8/28/2023 3,435,553 13.78% 19,375,685 20,607,144 13,808,148 23,820,687 25,312,644 24,922,764 0 0.00% 20,029,499 20,695,054 15,713,676 21,896,095 25,711,154 24,002,925 0 0 0.00% 21,1762,13 22,66187 15,337,370 25,390,777 27,64,642 26,46,574 0 0 0.00% 3,646,732 3,532,907 4,523,961 | 2019 2020 2021 2022 2023 2024 2024 2024 Actual Actual Actual Actual Collections Collection | 2019 2020 2021 2022 2023 2024 <th< td=""><td>2019 2020 2021 2022 2023 2024 2024 Collections Received Received</td><td>2019 2020 2021 2022 2023 2024 2024 Actual
Actual
Actual
Collections Actual
Actual
Collections Actual
Collections Collections 2024 2024 Actual
Actual
Actual
Collections Actual
Collections Collections 2024 Actual
Actual
Actual
Collections Actual
Collections Collections <thcolections< th=""> Collections</thcolections<></td><td>2019 2020 2021 2022 2023 2024 2024 Date Actual VErogettion Actual VErogettion Vert To Date Vert</td></th<> | 2019 2020 2021 2022 2023 2024 2024 Collections Received Received | 2019 2020 2021 2022 2023 2024 2024 Actual
Actual
Actual
Collections Actual
Actual
Collections Actual
Collections Collections 2024 2024 Actual
Actual
Actual
Collections Actual
Collections Collections 2024 Actual
Actual
Actual
Collections Actual
Collections Collections Collections <thcolections< th=""> Collections</thcolections<> | 2019 2020 2021 2022 2023 2024 2024 Date Actual VErogettion Actual VErogettion Vert To Date Vert |

Orange County Public Schools Sales Tax Collection History

nt
842,740
701,456
353,778
421,562
597,436
190,269
176,278
843,957
594,345
826,444
301,579
770,163
540,613
024,409
873,477
649,248
456,899
965,180
647,866
412,105
290,467
368,958 *
849,227

* Amount collected thru June 2023

Impact Fees Collections

	FY19	FY20	FY21	FY22	FY23	FY24
July	(1,356,434)	(791,922)	(15,459)	(1,326,589)	0	(6,763,808)
August	1,544,905	1,642,692	3,021,080	2,198,714	651,853	10,215,383
September	4,802,716	6,418,111	4,902,480	282,676	1,211,965	20,915
October	12,782,279	5,018,829	11,324,673	15,541,805	18,406,599	
November	764,538	11,783,397	744,321	3,824,286	626,571	
December	544,774	531,273	1,049,444	2,896,867	18,822	
January	14,550,401	1,435,048	56,625	14,137,661	16,638,979	
February	3,319,118	11,250,567	3,010,120	3,056,570	645,056	
March	929,755	1,613,436	3,125,497	2,347,260	2,677,874	
April	11,439,392	10,735,683	6,887,734	4,786,133	3,909,942	
May	674,261	2,027,236	5,720,199	16,810,116	25,302,244	
June	14,645,906	14,200,335	21,268,703	26,769,895	12,949,506	
Total	64,641,613	65,864,685	61,095,416	91,325,395	83,039,410	3,472,490

As of 9-11-23

MASTER SCHEDULE UPDATE

Capital Program Schedule Summary

	Sep-2023	Sep-2024	Sep-2025	Sep-2026	Sep-202	.7 S	ep-2028
Comprehensive Projects							
Lake Buena Vista HS/ Horizon HS (CT	E Lab 🗾 Nov-2	23					
Three Points ES Comprehe	nsive	Feb-24	Jun-25				
Howard MS Comprehe	nsive			Dec-25			
FY22 Multi-Site Comprehensive Renov	ation	Aug-24		Apr-26		Legend	
Winter Park HS Comprehe			Feb-25	May-26			
Windermere HS (On-Campus Stat			Feb-25	May-26		Planning	
Lakeview MS Comprehe				May-26		Design	
Colonial HS Comprehe		Jun-24		Jun-26		Construction	
Northlake Park ES Comprehe		/-23	Apr-25		Oct-26	Construction	
Ocoee MS Comprehe		/-23	Jun-25		Dec-26		
Lawton Chiles ES Comprehe		c-23	Jun-25		Dec-26		
Oakshire ES Comprehe		an-24	Jun-25		Dec-26		
Palmetto ES Comprehe		Jan-24	Jun-25		Dec-26		
Chain of Lakes MS Comprehe		Mar-24	Sep	-25	Jul-27	,	
Olympia HS Comprehe		Jun-24		ov-25	Jul-2		
Boone HS Comprehe		May-24		lov-25	Jul-2		
Timber Creek HS Comp & Capacity Enhance		Apr-24	Sec		Jul-2		
Jones HS Comprehe		May-24		ov-25	Jul-2		
Capacity Enhancement Projects							
4-Site SY 2024-25 ES Capacity Enhance	ment	Feb-24	Jun-25				
Oak Ridge HS Capacity Enhance	ment	Aug-24	Jul-25				
4-Site SY 2024-25 MS Capacity Enhance	ment	Feb-24	Jul-25				
Relief Projects							
47-E-W-4 Horizon West/ Village "H"		Jun-24					
129-M-SE-2 Laureate Park South, Lake Nona		Jun-24					
50-H-SE-2 Meridian Park		Sep-					
130-E-SE-2 Laureate Park South, Lake Nona		an-24	Jun-25				
97-E-SE-2 Weewahootee	Area	Jul-24	Jul-25				
Repurpose Projects		_					
Clarcona (Old) Demo							
Cherokee School (Repur		May-24	May-25				
121-A-N-7 West Bus Comp			Feb-25	May-26			
Esteem Academy (Multi-System Ren			Feb-25	Jun-26			
Kaley ESE Services (Multi-System Ren	ewal)	Apr-24	Ser	-25	Dec-26		
Technical College Projects							
Hungerford ES (Bl							
Orlando Technical College Comprehe		Feb-24					
73-T-W-7 - OTC West Ca		Feb-24					
OTC - East Campus Replace			Dec-24				
OTC - South Campus Replace	ment		Sep-2	25	May-27		

PROJECT BUDGET UPDATE



PROJECT STATUS SUMMARY REPORT

NEW AND REPLACEMENT SCHOOLS

							September 21, 2	023										
Funding Source(s)	Priority #	School Name	F1 FY 2023 Board Adopted Budget	· · ·	F3 FY 2024 Board Tentative Budget	Estimated Cost At Completion	Variance	GMP Amount	F4 Construction Change Orde		F5 ODP Change Ord	ders	Const	proved truction Contract Subst.	Days Past	Contract Type	CM / GC Firm	AE Firm
				Budget		completion			Amount	#	Deducts	#	Construct	Com	Substantial (Close-out)			
						B	udget							Schedule			Contracti	ng
PLANNING PHASE																		
Impact	New	Site 126-E-W-4		45,535,000	45,535,000	45,535,000	-											
propoerty	New	Site 136-A-E-5 (NE Maint Repl)		20,000,000	20,000,000	20,000,000	-											
		Sub Total	-	65,535,000	65,535,000	65,535,000	-											
DESIGN PHASE																		
ST, Impact		Site 97-E-SE-2	38,695,000	6,927,000	45,622,000	45,622,000	-										Welbro	Schenkel
CIT	New	Site 121-A-W-7 (West Bus Compound)	36,004,000	7,201,000	43,205,000	43,205,000	-										Pirtle	Spiezle
Impact	New	Site 130-E-SE-2	41,124,000	4,498,000	45,622,000	45,622,000	-										TBD	Schenkel
				10.000.000														
		Sub Total	115,823,000	18,626,000	134,449,000	134,449,000	-											
CONSTRUCTION PI	-		44.005.000		44.005.000	44.005.000		26.072.022			(5.004.542)	2	7/42/2022	6/24/2024		CI 4D		
Impact	New	Site 47-E-W-4	44,995,000	-	44,995,000	44,995,000	-	36,973,822			(5,004,542)	2	7/12/2023	6/21/2024		GMP	Welbro	Schenkel
Sales Tax		Hungerford ES (renov Bldg 8)	6,720,000	-	6,720,000	6,720,000	-	3,836,726		4.2	(631,727)	1	11/11/2022	9/5/2023		GMP	Johnson Laux	Schenkel
ST, Impact, CIT		Site 50-H-SE-2	230,000,000	-	230,000,000	230,000,000	-	198,036,960	· · · ·	12	(33,140,287)	5	8/29/2022	9/30/2024		GMP	CORE	Zyscovich
Sales Tax CIT		Site 73-T-W-7 (OTC West Campus) Site 129-M-SE-2	64,805,000 79,433,000	-	64,805,000 79,433,000	64,805,000 79,433,000	-	48,931,894 68,597,308	190,003	2	(12,235,000) (17,690,998)	2	8/26/2022 2/23/2023	1/31/2024 6/28/2024		GMP GMP	Wharton Walker	DLR Group Schenkel
Sales Tax	-	Site 512-T-E-1 (OTC East Campus)	63,994,000	-	63,994,000	63,994,000	-	50,325,542	-		(10,973,569)	2 1	6/1/2023	12/17/2024		GMP	CPPI	DLR Group
Jales Tax	135		03,994,000	-	03,994,000	03,994,000	-	50,525,542	-		(10,973,309)	1	0/1/2023	12/17/2024		Givir	CPPI	DLK Group
		Sub Total	489,947,000	-	489,947,000	489,947,000	-	406,702,253	(79,383)	14	(79,676,123)	13						
CLOSE OUT PHASE								. ,			,			Actual				
Impact	New	Water Spring MS (Site 65-M-W-4)	50,480,000	-	50,480,000	50,480,000	-	42,828,832	-		(15,548,150)	4	11/15/2021	8/1/2023	51	GMP	CORE	Harvard Jolly
		Sub Total	50,480,000	-	50,480,000	50,480,000	-	42,828,832	-	-	(15,548,150)	4						
L	I	Grand Total	656,250,000	84,161,000	740,411,000	740,411,000	-	449,531,085	(79,383)	14	(95,224,273)		I					

Footnotes

F1 - Reflects the FY2023 10yr Capital Budget dated September 2022.

F2 - Reflects changes between the FY 2024 and the FY 2023 adopted budget.

F3 - Reflects the Capital Program Tentative Budget for FY 2024.

F4 - Reflects number of change orders and cumulative change order amount. Does not include ODP deductive and reconciliation change orders.

F5 - Reflects the amount and number of ODP deductive and reconciliation change orders to date.

F6 - Reflects number of days beyond substantial completion. See justification below under Close Out Delays.

Completion Delays

Hungerford ES (renov Bldg 8) - CM's request for time extension is curently being reviewed.

Close Out Delays

None

Funding Source	Priority #	School Name	Explanation of Adopted Budget Changes
PLANNING PHASE			
Impact	New	Site 126-E-W-4	Added Project
propoerty	New	Site 136-A-E-5 (NE Maint Repl)	Added Project
DESIGN PHASE			
ST, Impact	New	Site 97-E-SE-2	Estimate updated to reflect overall program requirements and current market conditions.
CIT	New	Site 121-A-W-7 (West Bus Compound)	Estimate updated to reflect overall program requirements and current market conditions.
Impact	New	Site 130-E-SE-2	Estimate updated to reflect overall program requirements and current market conditions.

Other

Projects Closed Since Last Report

Panther Lake ES (Site 114-E-W-4)

Final Budget Variance (\$519,000) Final ODP % 30.6%

13



PROJECT STATUS SUMMARY REPORT

COMPREHENSIVE SCHOOLS

								nber 21, 2023										
Funding Source	Priority	School Name	F1	F2	F3	Estimated	Variance	GMP	F4		F5			roved	F6	1	CM / GC Firm	AE Firm
	#		FY 2023 Board	Changes from	FY 2024 Board	Cost At		Amount	Construction	n	ODP Change Ord	lers	Constr	ruction	Number of	Туре		1
			Adopted Budget	FY 2023	Tentative Budget	Completion		_	Change Orde	ers					Days Past			1
				Adopted					Amount	#	Deducts	#	NTP	Contract	Substantial			1
				Budget									Construct	Subst. Com	(Close-out)			
							Budget							Schedule			Contractin	g
Sales Tax		Boone HS		79,589,000	79,589,000	79,589,000												
Sales Tax		Chain of Lakes MS	38,920,200	13,279,800	52,200,000	52,200,000	-											
CIT, Sales Tax		Cherokee School (Repurpose)	24,960,000	42,040,000	67,000,000	67,000,000												
CIT, Sales Tax		Clarcona (Old) Demolition	1,277,000	42,040,000	1,277,000	1,277,000												
CIT		Esteem Academy (Repurpose)	30,203,000	19,919,000	50,122,000	50,122,000												
Sales Tax		Jones HS	30,203,000	61,026,000	61,026,000	61,026,000												
CIT		Kaley ESE Services (Repurpose)	16,832,000	3,366,000	20,198,000	20,198,000												
Sales Tax		Lawton Chiles ES	24,672,900	7,427,100	32,100,000	32,100,000												
Sales Tax		Northlake Park ES	36,555,900	7,994,100	44,550,000	44,550,000	-											
Sales Tax		Oakshire ES	24,812,400	2,687,600	27,500,000	27,500,000	-											
Sales Tax		Ocoee MS	40,557,000	20,007,000	60,564,000	60,564,000												
Sales Tax		Odyssey MS	40,557,000	47,733,000	47,733,000	47,733,000												
Sales Tax		Olympia HS		98,682,000	98,682,000	98,682,000												
Sales Tax		Palmetto ES	32,393,400	8,106,600	40,500,000	40,500,000												
Sales, Property		Timber Creek HS (Comprehensive)	32,333,400	90,587,000	90,587,000	90,587,000												
Tax				50,507,000	50,507,000	50,507,000												1
Тах		Sub Total	271,183,800	502,444,200	773,628,000	773,628,000	-											·
DESIGN PHASE			2/1/100/000	502) 11,200	770,020,000	110)020)000												
Sales Tax		Colonial HS	96,419,000	1,236,000	97,655,000	97,655,000	-										Wharton	Schenkel
Sales Tax		FY22 Multi-Site Comprehensive Reno	96,624,000	-	96,624,000	96,624,000	-										Wharton	Zyscovich
Sales Tax		Lakeview MS	44,809,000	4,082,000	48,891,000	48,891,000	-										Wharton	Song + Assoc.
Sales Tax		Oak Ridge HS Functional Equity	15,221,000	5,529,000	20,750,000	20,750,000	-											
Sales Tax	133	OTC South Campus	82,600,000	114,400,000	197,000,000	197,000,000	-										Williams	Harvard Jolly
Sales Tax		SY 2024-25 ES Functional Equity	31,000,000	3,109,000	34,109,000	34,109,000	-										McCree	C.T. Hsu
Sales Tax		SY 2024-25 MS Functional Equity	42,700,000	3,867,000	46,567,000	46,567,000	-										Thorton	Little
Sales Tax		Three Points ES	21,974,000	851,000	22,825,000	22,825,000	-										OHL	C.T. Hsu
Sales Tax		Windermere HS (On-Campus Stadium)	6,800,000	-	6,800,000	6,800,000	-										Wharton	Schenkel
Sales Tax		Winter Park HS	89,722,000	1,181,000	90,903,000	90,903,000	-										CPPI	C.T. Hsu
		Sub Total	527,869,000	134,255,000	662,124,000	662,124,000	-											·
CONSTRUCTION PH	HASE																	
Sales Tax		Howard MS	55,063,000	5,768,000	60,831,000	60,831,000	-	45,106,554			(10,662,670)	1	6/12/2023	12/1/2025		GMP	Lego	Rhodes + Brito
Sales Tax		Orange Technical College	47,020,000	-	47,020,000	47,020,000	-	35,352,358	167,047	2	(5,932,626)	1		12/11/2023		GMP	Gilbane	Harvard Jolly
Sales Tax		Lake Buena Vista HS/ Horizon HS (CTE Lab Conversions & Misc.)	3,476,000	-	3,476,000	3,476,000	-	1,236,791	-	-	(131,608)	1	3/16/2023	11/10/2023		GMP	Wharton	Schenkel
		Sub Total	222,654,000	117,095,000	111,327,000	111,327,000	-	81,695,703	167,047	2	(16,726,904)	3						
CLOSE OUT PHASE														Actual				
		Sub Total	-	-	-	-	-	-	-	-	-	-						
		Grand Total	1,021,706,800	753,794,200	1,547,079,000	1,547,079,000	-	81,695,703	167,047	2	(16,726,904)	3						

Footnotes

F1 - Reflects the FY2023 10yr Capital Budget dated September 2022.

F2 - Reflects changes between the FY 2024 and the FY 2023 adopted budget.

F3 - Reflects the Capital Program Tentative Budget for FY 2024.

F4 - Reflects number of change orders and cumulative change order amount. Does not include ODP deductive and reconciliation change orders.

F5 - Reflects the amount and number of ODP deductive and reconciliation change orders to date.

F6 - Reflects number of days beyond substantial completion. See justification below under Close Out Delays.

Completion Delays

None

Close Out Delays

None

- Multiple Sites Projects
 - Westridge MS
- Whispering Oak ES.

and Endeavor ES.

Projects Closed Since Last Report

None

1. SY 2024-25 MS Functional Equity includes improvements at 3 sites: College Park MS, Hunters Creek MS, and 2. SY 2024-25 ES Functional Equity includes improvements at 3 sites: Dr. Phillips ES, Hunters Creek ES, and 3. FY22 Multi-Site Comprehensive Renovation includes improvements at 4 sites: Avalon ES, Camelot ES, Citrus ES,

Final Budget Variance

Final ODP %



COMPREHENSIVE SCHOOLS

c	ont	om	hor	21	2023	

Funding Source	Priority #	School Name	Explanation of Adopted Budget Changes
PLANNING PHASE			
Sales Tax		Boone HS	Added project
Sales Tax		Chain of Lakes MS	Estimate updated to reflect overall program requirements and current market conditions.
CIT, Sales Tax		Cherokee School (Repurpose)	Estimate updated to reflect overall program requirements and current market conditions.
CIT		Esteem Academy (Repurpose)	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Jones HS	Added project
CIT		Kaley ESE Services (Repurpose)	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Lawton Chiles ES	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Northlake Park ES	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Oakshire ES	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Ocoee MS	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Odyssey MS	Added project
Sales Tax		Olympia HS	Added project
Sales Tax		Palmetto ES	Estimate updated to reflect overall program requirements and current market conditions.
Sales, Property Tax	(Timber Creek HS (Comprehensive)	Added project
DESIGN PHASE			
Sales Tax		Colonial HS	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Lakeview MS	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Oak Ridge HS Functional Equity	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax	133	OTC South Campus	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		SY 2024-25 ES Functional Equity	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		SY 2024-25 MS Functional Equity	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Three Points ES	Estimate updated to reflect overall program requirements and current market conditions.
Sales Tax		Winter Park HS	Estimate updated to reflect overall program requirements and current market conditions.
CONSTRUCTION P	HASE		
Sales Tax		Howard MS	Estimate updated to reflect overall program requirements and current market conditions.





Project Status Summary Report

Capital Renewal Projects (Note 1)

September 21, 2023

					Pro	oject E	Eleme	nts					September	21, 2025									Sm - Constr.	Amount < \$280K	
Location	Wt'd Age	Projec	:t	ng	tural	or anical	ical	afety	eyance alties	Prior Project	Project Budget	Current Project	Current Estimated Cost At	Variance from Current Project	GMP Amount	Constructio Change Ord		ODP Change Orde	rs		roved ruction	Number of Days Past Subst.	Contract Type	CM / GC Firm	AE Firm
	(FISH)	Number	Size	Site Roofir	Structura Exterior	Interior Mechani	Electr	Life S. Tachn	Conveyance Specialties	Budget	Changes	Budget	Completion	Budget	Amount	Amount	#	Deducts	#	NTP Construct	Contract Subst. Compl.	Compl. (close-out)			
														Budget							Schedule			Contracting	
PLANNING PHASE					· · ·																				
Dr Phillips HS	-	N0188.0	Int	✓	 ✓ 					-	2,223,000	2,223,000	2,223,000	-											
Dr Phillips HS	-	N0183.0	Sm				✓	· ·		75,000	-	75,000	75,000	-											
FY23 Multi-Site Exterior Painting	-	N0176.0	Int			~	✓			2,088,000	-	2,088,000	2,088,000	-											
FY23 Multi-Site Low Voltage CCTV	-	N0172.0	Lg					✓		4,089,000	-	4,089,000	4,089,000	-											
FY23 Multi-Site Chiller Coil Repl.	-	N0189.0	Int	×	✓	~	✓ ✓	´ ✓ ✓		-	1,100,000	1,100,000	1,100,000	-											
FY24 Multi-Site Carpet Replacement	-	N0190.0	Lg					✓		-	7,112,000	7,112,000	7,112,000	-											
Rosemont ES	23-Yr	N0090.2	Int	\checkmark	✓ ✓	✓		✓ v		-	352,352	352,352	352,352	-									+		
Rosemont ES Union Park MS	23-Yr 17-Yr	N0090.0	Lg		▼ ▼	v	v	• •		5,871,000	4,759,000	5,871,000 4,759,000	5,871,000 4,759,000	-											
University HS	17-11 13-Yr	N0191.0 N0177.0	Lg Int	vv	v			√		- 1,330,000	4,759,000	4,759,000	1,330,000	-											
	13-11	NU177.0						•		1,330,000	-	1,330,000	1,330,000	-											
SUBTOTAL (Pla	nning)	10 Proje	ote	36 5	Sitor					13,453,000	15,546,352	28,999,352	28,999,352										+		
DESIGN / PRE-CONSTRUCTION PH	0,	TO PTOJE		50 0	JILES					13,433,000	15,540,552	20,333,332	20,333,332	-											
Andover ES	18-Yr	N0124.0	Lg	✓		✓	✓			5,720,000	817,000	6,537,000	6,537,000	-										Lego Construction	OCI Engineering
Apopka HS	15-Yr	N0136.0	-	 ✓ ✓ 	 ✓ 	 ✓ 	✓	I		17,996,000	-	17,996,000	17,996,000	-										Bishop Construction	RGD
Evans HS	13-Yr	N0150.0	Sm				✓			232,000	-	232,000	232,000	-										TERM SERV	Voltair
FY22 LED Conversion Pilot at 03-Sites	-	N0159.0	Int				✓			2,536,000	-	2,536,000	2,536,000	-									1	Schmid Construction	Voltair
FY22 Exterior Painting Group 1	-	N0123.0	Int		✓					2,325,000	-	2,325,000	2,325,000	-										TBD	Gale
FY22 Exterior Painting Group 2	-	N0162.0	Lg		✓					3,357,000	-	3,357,000	3,357,000	-										TBD	Gale
HVAC at 02-Sites	-	N0125.0	Lg	\checkmark		✓		✓		3,700,000	5,337,000	9,037,000	9,037,000	-										Lego Construction	GRāEF-USA
HVAC at 02-Sites	-	N0139.0	Lg			✓				22,289,000	-	22,289,000	22,289,000	-										Johnson-Laux	TLC Engineering
HVAC at 02-Sites	-	N0140.0	Lg				✓			22,872,000	-	22,872,000	22,872,000	-										McCree	OCI Engineering
HVAC at 03-Sites	-	N0168.0	Lg	✓	✓	✓				32,047,000	-	32,047,000	32,047,000	-										T&G Constructors	OCI Engineering
HVAC at 05-Sites	-	N0105.0	Lg				 			21,357,000	-	21,357,000	21,357,000	-										Lego Construction	Matern
HVAC at 06-Sites	-	N0147.0	Lg			 ✓ 				13,658,000	-	13,658,000	13,658,000	-										Sequel Developers	GRāEF-USA
Lockhart MS	15-Yr	N0138.0	Lg	~		✓	~			6,890,000	-	6,890,000	6,890,000	-										Votum	Baker Barrios
Low Voltage at 38-Sites	-	N0120.0	Lg					✓ ✓		29,180,000	-	29,180,000	29,180,000	-										Johnson-Laux	Matern
Dommerich ES/ Maitland MS	-	N0137.0	Lg	 ✓ 	v	 ✓ 		✓✓		12,555,000	-	12,555,000	12,555,000	-										Welbro	SGM
Lakemont ES/ Windy Ridge K8	-	N0144.0	Lg	\checkmark	✓ ✓					18,799,000	-	18,799,000	18,799,000	-										Votum	SGM
Multi-System Group 1	-	N0142.0	Lg	v v	✓	 ✓ ✓ 	✓ ✓ ✓ ✓			32,262,000	-	32,262,000	32,262,000	-									╂────┼─	Wharton Smith	Matern
Ocoee HS Piedmont Lakes MS	18-Yr	N0099.0	Lg			✓ ✓ ✓				14,749,000	-	14,749,000	14,749,000	-									├ ───┼─	T&G Constructors CPPI	GRāEF-USA
	30-Yr	N0119.0	Lg	✓ ✓				· • •	/	17,690,000	-	17,690,000	17,690,000	-									++		Bobes Associate
Roberto Clemente MS Tildenville ES	20-Yr 19-Yr	N0111.0 N0131.0	Lg	v v						18,914,000 7,347,000	2,105,000	18,914,000 9,452,000	18,914,000 9,452,000	-									+	Votum Construction Johnson-Laux	SGM OCI
Union Park MS	19-11 17-Yr	N0131.0 N0132.0	Lg	\checkmark		▼ ▼				5,311,000	2,103,000	9,452,000 5,311,000	<u>9,452,000</u> 5,311,000	-									┣────┼─	Messam	Little Diversified
Westbrooke ES	17-Yr 15-Yr	N0132.0 N0155.0	Lg Lg			▼ ✓				5,064,000	-	5,064,000	5,064,000	-									++	Williams	GRāEF-USA
			-9							0,001,000		0,001,000	0,001,000										+		0.021 00/1
SUBTOTAL (Design/Pr	re-Con)	23 Proje	ects	76 5	Sites					319,464,000	8,259,000	325,109,000	325,109,000	-											

<u>Project Size Key</u> Lg - Constr. Amount > \$2M Int - Constr. Amount > \$280K and < \$2M Sm - Constr. Amount < \$280K



Project Status Summary Report

Capital Renewal Projects (Note 1)

September 21, 2023

					I	Proje	ct Elen	nents					September	21, 2025									Sm - Const	r. Amount < \$280K	
Location	Wt'd Age (FISH)	Projec Number		e ofing	tructural	cterior terior	chanical ctrical	umbing fe Safety	Technology Conveyance	S Prior Project Budget	Project Budget Changes	Current Project Budget	Current Estimated Cost At	Variance from Current Project	GMP Amount	Construction Change Orders	s (ODP Change Orders	s	Appr Constr	oved ruction Contract	Number of Days Past Subst. Compl.	Contract Type	CM / GC Firm	AE Firm
				Site Roo	Stru	Inte	Mec	Plur Life	Tec	Spe	_		Completion	Budget		Amount #	#	Deducts	# c	Construct	Subst. Compl.	(close-out)			
														Budget							Schedule			Contracting	
CONSTRUCTION PHASE																									
Chain of Lakes MS	25-Yr	N0076.1	Int				✓			1,036,000	-	1,036,000	1,036,000	-	726,813	-	-	-		03/11/22	11/30/23		TERM SERV	Trane	SGM
Chiller Repl at 02-Sites	-	N0101.0	Lg				 ✓ ✓ 			2,766,000	-	2,766,000	2,766,000	-	2,411,000	-	-	-		01/12/23	01/19/24		TERM SERV	Trane	GRāEF-USA
Dr Phillips HS	11-Yr	N0133.0	Lg	 ✓ 			\checkmark			4,302,000	-	4,302,000	4,302,000	-	3,645,995	-	-	(718,441)		02/09/23	04/29/24		GMP	HA Contracting	GRāEF-USA
Eagle's Nest ES	19-Yr	N0164.0	Sm	✓	•	✓	\checkmark			70,000	-	70,000	70,000	-	36,500	-	-	-		03/22/23	09/29/23		TERM SERV	Frank Gay	N/A
Edgewater HS	13-Yr	N0175.0	Sm				~			-	97,679	97,679	97,679	-	97,679	-	-	-		05/15/23	09/15/23		TERM SERV	Trane	N/A
Evans HS	13-Yr	N0166.0	Sm							156,000	-	156,000	156,000	-	123,104	-	-	-		01/20/23	02/16/24		TERM SERV	Trane	N/A
FY22 Low Voltage CCTV at 18-Sites	-	N0158.0	Lg						✓	5,472,000	-	5,472,000	5,472,000	-	1,508,380	-	-	-		11/03/22	10/02/23		TERM SERV	Archis	N/A
FY23 Multi-Site Low Voltage Sonitrol	-	N0171.0	Sm		+				✓	336,000	-	336,000	336,000	-	293,612	-	-	-		05/18/23	06/12/24		TERM SERV	Securitas	N/A
Chiller R'newal at 05-Sites	-	N0169.0	Lg				✓			2,470,000	151,000	2,621,000	2,621,000	-	2,465,372	-	-	-		03/14/23	03/15/24		TERM SERV	Multiple Vendors	N/A
Gotha MS	29-Yr	N0156.0	Int				✓			2,328,000	616,000	2,944,000	2,944,000	-	2,448,213	-	-	-		02/24/23	02/12/24		TERM SERV	Trane	Matern
Jones HS	19-Yr	N0059.3	Lg	✓						6,757,000	-	6,757,000	6,757,000	-	5,643,940	-	-	(1,665,725)		06/27/22	05/03/24		GMP	McCree	KBJ
Lake Silver ES	10-Yr	N0181.0	Sm	 ✓ 	•	✓				✓ -	59,966	59,966	59,966	-	59,966	-	-	-		05/11/23	09/15/23		TERM SERV	Shaw	N/A
Liberty MS	18-Yr	N0167.0	Int				✓			✓ 1,037,000	-	1,037,000	1,037,000	-	841,092	-	-	(396,183)		08/22/22	06/12/23		GMP	SkyBuilders USA	Baker Barrios
Audio Enhancement Intercom Pilot	-	N0180.0	Int					✓	✓	1,353,000	-	1,353,000	1,353,000	-	1,060,274	-	-	-	-	06/20/23	05/01/24		TERM SERV	Audio Enhancement	N/A
NW Maint (Old Maxey)	55-Yr	N0173.0	Sm							175,949	-	175,949	175,949	-	175,949	-	-	-		06/19/23	02/13/24		TERM SERV	Air Mechanical	N/A
OCPS ACE	7-Yr	N0186.0	Sm			✓	✓	✓	✓	-	301,000	301,000	301,000	-	159,601	-	-	-	-	07/18/23	12/15/23		TERM SERV	Rauland-Borg	N/A
Pinewood ES	26-Yr	N0179.0	Int	 ✓ 						-	373,292	373,292	373,292	-	373,292	-	-	-		05/09/23	04/01/24		TERM SERV	Ovation	N/A
Roofing at 02-Sites	-	N0103.0	Lg	✓				✓		10,259,000	-	10,259,000	10,259,000	-	8,972,425	-	-	(2,953,310)	1	02/02/23	12/09/24		GMP	CORE	Raymond
Roofing at 04-Sites	-	N0102.0	Lg	✓						3,125,000	-	3,125,000	3,125,000	-	2,711,534	-	-	(679,895)	2	08/05/22	12/15/23		GMP	Lego Construction	Gale
Thornebrooke ES	20-Yr	N0091.0	Lg					✓	✓	4,668,000	-	4,668,000	4,668,000	-	3,885,167	-	-	(236,449)	2	11/04/22	10/13/23		GMP	CPPI	GRāEF-USA
Chiller Repl at 04-Sites	-	N0151.0	Lg				< <			3,453,000	523,000	3,976,000	3,976,000	-	2,681,020	-	-	-	-	08/14/24	02/28/25		TERM SERV	Carrier	TLC
West Oaks ES	18-Yr	N0143.16	Sm	✓						103,000	-	103,000	103,000	-	78,051	-	-	-	-	03/07/23	10/12/23		TERM SERV	Atlas Apex	N/A
Washington Shores PLC	17-Yr	N0184.0	Sm	✓	•	✓				-	375,000	375,000	375,000	-	245,420	-	-	-	-	06/20/23	12/15/23		TERM SERV	Ovation	N/A
Wekiva HS	16-Yr	N0174.0	Sm	 ✓ 	•	✓	✓			-	67,377	67,377	67,377	-	67,377	-	-	-	-	05/01/23	09/15/23		TERM SERV	TERM SERV	n/a
Windy Ridge K8	17-Yr	N0178.0	Int	 ✓ 						-	328,648	328,648	328,648	-	328,648	-	-	-	-	05/17/23	04/01/24		TERM SERV	Sequel	N/A
SUBTOTAL (Constr	ruction)	25 Proje	ects	51	Sites					49,866,949	2,892,962	52,759,911	52,759,911	-	41,040,423	-	-	(6,650,004)	9						
SUBTOTAL (Active)		58 Proje	ects	108	Sites	i				382,783,949	26,698,314	406,868,263	406,868,263	-	41,040,423	-	-	(6,650,004)	9						
CLOSE-OUT																					Actual				
Boone HS	23-Yr	N0031.8	Sm				 ✓ 			389,000	-	389,000	389,000	-	278,628	-	-	-	-	05/15/23	08/14/23	38	GMP	Ovation	CPH Inc.
Lakeview MS	23-Yr	N0102.1	Lg	 ✓ 						3,120,000	-	3,120,000	3,120,000	-	2,687,401	-	-	-	-	02/23/22	08/14/23	38	TERM SERV	Atlas Apex	Gale
Liberty MS	18-Yr	N0141.0	Int			✓		×		2,614,000	472,000	3,086,000	3,086,000	-	2,272,159	-	-	-	-	06/02/23	08/22/23	30	GMP	SkyBuilders USA	Baker Barrios
FY22 Low Voltage Intrusion Detection at 05-Sites	-	N0161.0	Int						~	600,000	-	600,000	600,000	-	564,349	-	-	-		03/03/23	08/02/23	50	TERM SERV	Securitas	N/A
Riverdale ES	25-Yr	N0170.0	Int			✓				600,000	144,000	744,000	744,000	-	572,478	-	-	-	-	02/22/23	08/11/23	41	TERM SERV	Multiple Vendors	N/A
SUBTOTAL (Clos	se-Out)	5 Proje	cts	9 9	Sites					7,323,000	616,000	7,939,000	7,939,000	-	6,375,016	-	-	-	-						

Notes
1. Capital Renewal is the replacement of major systems and components needed to preserve the efficient operation of school facilities. Capital Renewal funds are intended for Groups G3, G4, G5, and G6 school facilities, and Project Elements greater than \$50,000 in Priorities P1, P2, and P3 (and incidental P4 or P5 Elements).

Completion Delays

None

Projects Closed Since Last Report

Timber Creek HS (N0037.4)

Close Out Delays

None

1. The GMP amount for FY22 Low Voltage CCTV at 18-Sites is an estimated amount which will be updated as Term Service purchase orders are executed.

<u>Project Size Key</u> Lg - Constr. Amount > \$2M Int - Constr. Amount > \$280K and < \$2M

Sm - Constr. Amount < \$280K

Final Budget Variance

N/A

Final ODP % N/A



Project Status Summary Report

Capital Renewal Projects (Note 1)

September 21, 2023

			Project Elements											Sill - Collist	1. Amount > \$200K	
Location	Wt'd Age (FISH)		Site Site Structural Exterior Interior Mechanical Electrical Electrical Delumbing Life Safety Conveyance Specialties Specialties	Current Project Budget	Current Estimated Cost At	Variance from Current Project	GMP Amount	Construction Change Orders	OD Change		Appro Constr		Number of Days Past Subst. Compl.	Contract Type	CM / GC Firm	AE Firm
	(11311)		Specence Specer Structure	Budget	Completion	Budget		Amount #	Deducts	; #	NTP Construct	Subst.	(close-out)			
						Budget						Compl. Schedule)		Contracting	
Location		Project	Explanation of Project Budget Changes		Multiple Sites	Projects, with Fl	orida Invent	ory of School Houses	(FISH) Wt'd	Age in [[brackets]:					
		Number Size	9	1	1. N0101.0 cons	ists of chiller repl	acement at 2	campuses: Roberto	Clemente MS	[20] an	nd Lake Sybelia	ES [14].				
PLANNING PHASE				2	2. N0102.0 cons	ists of select roof	replacement	at 3 campuses: Sad	er ES [38], V	/inderme	ere ES [17], and	d Windy Rid	ge K8 [17].			
Dr Phillips HS	-	N0188.0 Int	Added project	3	3. N0103.0 cons	sts of select roof	replacement	at 2 campuses: Aval	on MS [17] a	nd Mead	dowbrook MS [1	18].				
FY23 Multi-Site Chiller Coil Repl.	-	N0189.0 Int	Added project	4	4. N0105.0 cons	sts of select HVA	C replaceme	ent at 5 campuses: Ca	astle Creek E	S [17], C	Columbia ES [1	6], West Oa	ks ES [19], Win	dermere ES [17],	and Wolf Lake ES [1	17].
FY24 Multi-Site Carpet Replacement	-	N0190.0 Lg	Added project	5				alarm, intercom, and/								
Rosemont ES	23-Yr	N0090.2 Int	Added project					[20]; East Lake ES [´ IS [18]; Maitland MS								
Union Park MS	17-Yr	N0191.0 Lg	Added project					38]; Sand Lake ES [1							e ES [13]; Waterford	ES [15]; West C
DESIGN / PRE-CONSTRUCTION P	PHASE				ES [19]; West	Orange HS [15];	vvindermere	ES [17]; Windy Ridge	e K8 [17]; WC	IT Lake	ES [17]; Wolf L	аке мъ [17]	; vvyndnam Lai	(es ES [17].		
Andover ES		N0124.0 Lg	Budget adjustment per submitted GMP.	- 6	6. N0123.0 cons	ists of exterior pa	inting at 17 c	ampuses: Aloma ES	[11]; Azalea l	Park ES	[12]; Cypress S	Springs ES [[12]; Forsyth Wo	oods ES [13]; Lak	e Sybelia ES [14]; La	ancaster ES [12];
HVAC at 02-Sites	-	N0125.0 Lg	Budget adjustment per refined scope of work and estimated construction cost.			[11]; Princeton E es ES [17]; Zellw		Springs ES [12]; Sad	ler ES [38]; S	and Lak	ke ES [18]; She	nandoah ES	6 [16]; Southwo	od ES [26]; Sunrid	lge ES [11]; Wetherb	bee ES [12];
					Wynunain Lar	.es Lo [17], Zeliw	000 LO [12].									
Tildenville ES	19-Yr	N0131.0 Lg	Budget adjustment per refined scope of work and estimated construction cost.	7	7. N0125.0 cons	ists of select HVA	C replaceme	ent at 2 campuses: Di	llard Street E	S [19] a	ind Hiawassee E	ES [20].				
CONSTRUCTION PHASE				٤	3. N0137.0 cons	ists of multi-syste	m improveme	ents at 2 campuses: I	Dommerich E	S [14] a	and Maitland MS	S [14].				
Edgewater HS	13-Yr	N0175.0 Sm	Added project	9	9. N0139.0 cons	sts of select HVA	C replaceme	ent at 2 campuses: W	ekiva HS [16	and W	est Orange HS	[15].				
Chiller R'newal at 05-Sites	-	N0169.0 Lg	Budget adjustment per submitted vendor pricing.	10). N0140.0 cons	sts of select HVA	C replaceme	ent at 2 campuses: Ea	ast River HS	[14] and	l Lake Nona HS	[14].				
Gotha MS	29-Yr	N0156.0 Int	Budget adjustment per submitted vendor pricing.	11	1. N0142.0 cons	ists of multi-syste	m improveme	ents at 5 campuses: (Columbia ES	[16]; Mo	oss Park ES [16	6]; Stone Lal	kes ES [17]; Vis	ta Lakes ES [17];	West Creek ES [19]	l.
Lake Silver ES	10-Yr	N0181.0 Sm	Added project	12	2. N0144.0 cons	ists of multi-syste	m improveme	ents at 2 campuses: l	_akemont ES	[15]; W	/indy Ridge K8 [[17]				
OCPS ACE	7-Yr	N0186.0 Sm	Added project	13		ists of select HVA	C replaceme	ent at 7 campuses: Ba	aldwin Park E	S [16]; E	Eagle's Nest ES	6 [20]; McCo	y ES [18]; Mille	nnia ES [17]; Whi	spering Oak ES [18];	; Wyndham Lake
Pinewood ES	26-Yr	N0179.0 Int	Added project		ES [17].											
Chiller Repl at 04-Sites	-	N0151.0 Lg	Budget adjustment per submitted vendor pricing.	14	4. N0151.0 cons	ists of chiller repla	acement at 4	campuses: Killarney	ES [14]; Rob	inswood	d MS [15]; Timb	er Lakes ES	[15]; Walker M	IS [13].		
Washington Shores PLC	17-Yr	N0184.0 Sm	Added project		[10]; Forsyth V	Voods ES [13]; K	eene's Cross	replacement at 18 c ing [14]; Lake Nona N shington Shores PLC	/IS [12]; Land							
Wekiva HS	16-Yr	N0174.0 Sm	Added project		6. N0159.0 cons	sts of LED retrofi	t at 3 campus	ses: Freedom MS [18]; Freedom H	IS [20]; \	West Creek ES	[19].				
Windy Ridge K8	17-Yr	N0178.0 Int	Added project	17	7. N0161.0 cons	ists of intrusion d	etection syste	em replacement at 5	campuses: A	oopka 9	GC [28]; Castle	Creek ES [17]; Catalina E	6 [16]; Conway ES	6 [16]; Wekiva HS [16	6].
CLOSE-OUT				18		sts of exterior pa dge MS [11]; We	•	mpuses: Acceleratior [2].	East [21]; A	popka 9	IGC [28]; Apopk	a HS [15]; E	Edgewater HS [[·]	13]; Evans HS [13]; Hunter's Creek MS	6 [30]; South Cree
Liberty MS	18-Yr	N0141.0 Int	Budget adjustment per pending construction change orders.	19	9. N0168.0 cons	ists of select HVA	C replaceme	ent at 3 campuses: Bo	onneville ES	22]; Leg	gacy MS [18]; W	ashington S	Shores PLC [17].		
Riverdale ES	25-Yr	N0170.0 Int	Budget adjustment per submitted vendor pricing for additional scope req's.	20). N0169.0 cons	ists of chiller r'nev	val at 5 camp	ouses: Freedom MS [18]; Meadow	orook M	IS [18]; Olympia	1 HS [23]; Tir	mber Creek HS	[24]; Winter Park	9GC [13].	
		1		21	1. N0171.0 cons	ists of intrusion d	etection syste	em replacement at 4	campuses: A	ccelerati	ion East [21]; A	ndover ES [18]; Bay Meado	ows ES [20]; Chen	ey ES [17].	
				22	2. N0172.0 cons	sts of CCTV sec	urity cameras	replacement at 14 c	ampuses: Alo	ma ES	[11]; Azalea Pa	rk ES [12]; E	Bonneville ES [2	22]; Brookshire ES	[10]; Cypress Sprin	igs ES [12]; 2]: Zollwood ES [

23. N0176.0 consists of exterior painting at 7 campuses: Arbor Ridge K8 [11]; Brookshire ES [10]; Colonial 9GC [22]; Freedom HS [20]; Freedom MS [18]; Lakeville ES [24]; Sun Blaze ES [10].

24. N0180.0 consists of audio enhancement intercom improvements at 3 campuses: Lake Nona HS [14]; Millennia Gardens ES [8]; and Sadler ES [38].

25. N0189.0 consists of chiller coil replacement at 3 campuses: Cypress Creek HS [9]; Dr. Phillips HS [11]; Hunter's Creek MS [30].

26. N0190.0 consists of carpet replacement at 14 campuses: Blankner K8 [22]; Dillard St ES [19]; Hiawassee ES [19]; Jones HS [19]; Lakeville ES [24]; McCoy ES [18]; Metrowest ES [11]; Olympia HS [23]; Orange Center ES [14]; Roberto Clemente MS [20]; Robinswood MS [15]; Stone Lakes ES [17]; Thornbrooke ES [20]; West Oaks ES [18].

Project Size Key Lg - Constr. Amount > \$2M Int - Constr. Amount > \$280K and < \$2M Sm - Constr. Amount < \$280K

N0172.0 consists of CCTV security cameras replacement at 14 campuses: Aloma ES [11]; Azalea Park ES [12]; Bonneville ES [22]; Brookshire ES [10]; Cypress Springs ES [12]; Edgewater HS [13]; Hunter's Creek ES [13]; Lake Sybelia ES [14]; Prairie Lake ES [10]; Rock Springs ES [12]; Sun Blaze ES [10]; Sunridge MS [11]; Wetherbee ES [12]; Zellwood ES [12].

OCPS MASTER CLOSEOUT REPORT




CAPITAL PROJECT

	Water
	Spring MS
Project Number	S-0097
Project Manager	Tamara Cox
Architect of Record	Harvard Jolly
Construction Manager	CORE
Substantial Completion	08/01/23
Closeout Complete (Exhibit H)	Dec '23

CLOSEOUT DELIVERABLE	
O & M Manuals	Completed
Environmental Closeout Manual	WIP
Warranty Certificates	Missing (169)
Master Consolidated Punch List (signed-off)	WIP
Return of Items Procured w/GRs (\$75+)	WIP
As-Built Drawings	WIP
As-Built Project Manuals	WIP
Record Drawings & Project Manuals	WIP
Certificate of Substantial Completion	WIP
Certificate of Occupancy	WIP
Attic Stock	Missing (15)
Training	Missing (36)
Specific Easements	WIP
Sustainability Letter & Score Card	WIP
OEF 564 - Cost Breakdown Info	WIP
Final CRs & COs (excluding ODP / GMP reconciliation)	WIP
Final ODP Reconciliation Change Order	WIP
Final GMP Reconciliation Change Order	WIP
Certificate of Final Inspection (CFI)	WIP
Final Pay Application	WIP

20230912 - Master Closeout Report

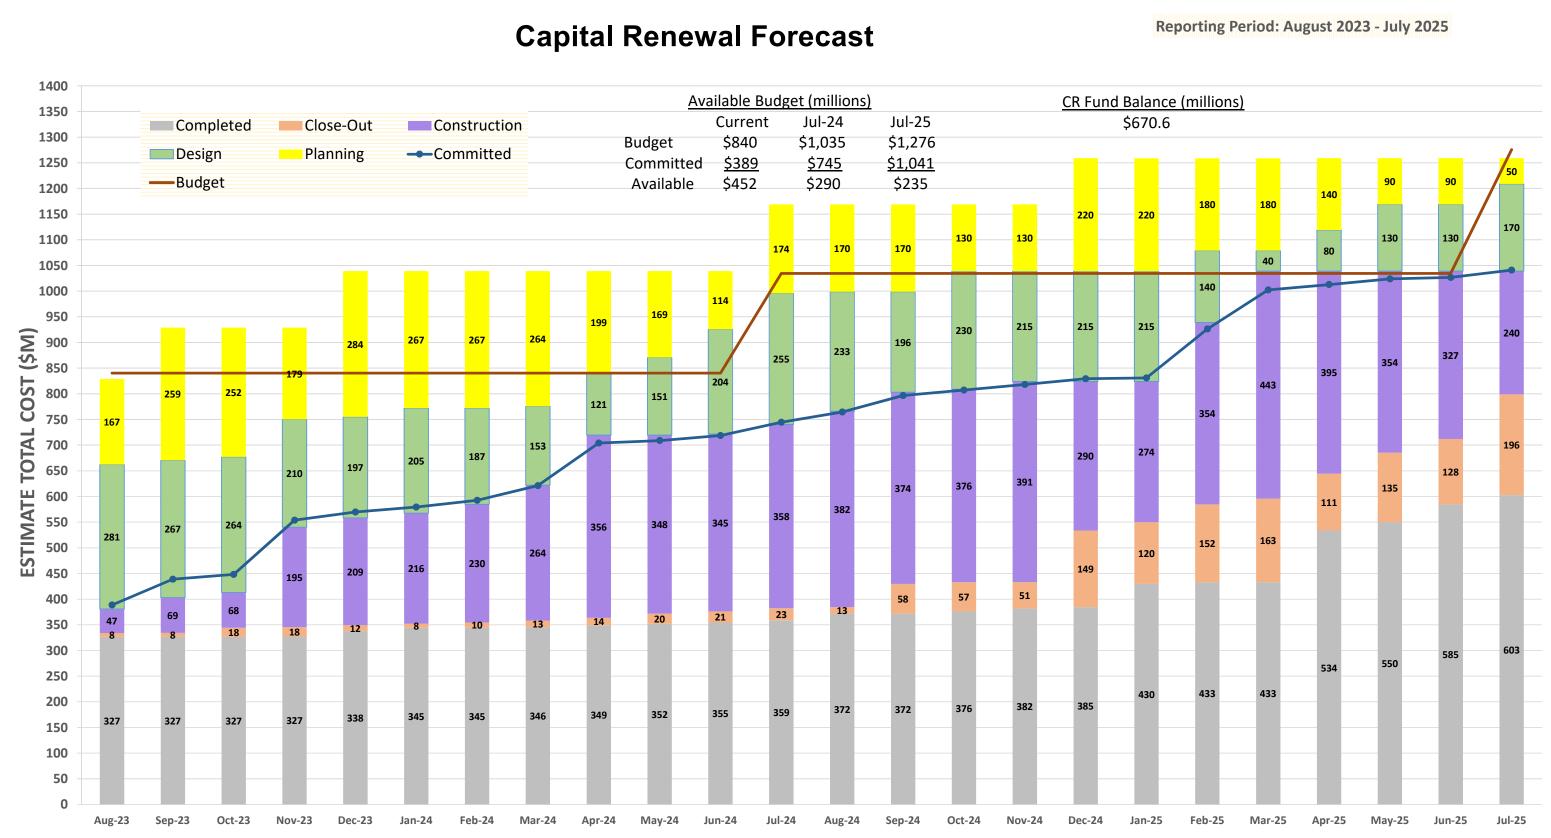

PROJECT STATUS REPORT

We continue with nine (9) projects under construction.

Three (3) Comprehensive Projects:


• Orange Technical College (Comprehensive Renovation)

Phase 1: Completed.

Phase 2: Includes the remaining half of floors 2-5, including roofing. Anticipated for completion late December 2023.

Project Status: Phase One work is complete. TCO has been issued. Phase Two work has started with demo of existing spaces and erection of new structural steel inside the building.

The project is forecasted to be complete late December 2023.

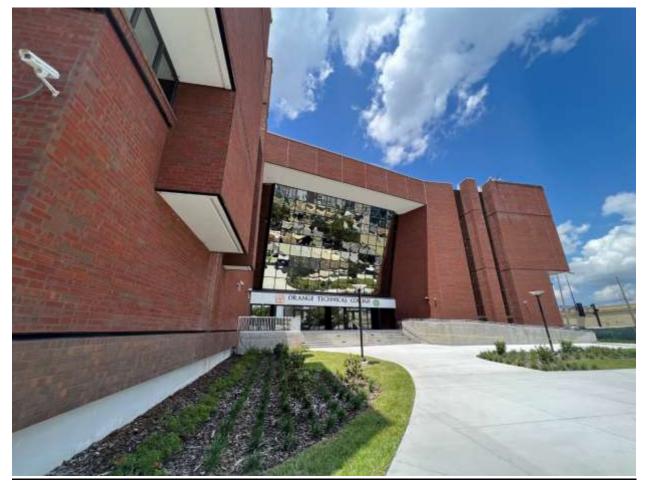

• Hungerford Building 8 (Comprehensive Renovation)

Select renovation of existing Hungerford Building 8 to convert into a welding lab/construction lab using classrooms, restrooms, and spaces for mechanical and electrical rooms. Existing metal covered play structure to be converted into outdoor welding school and added parking.

Project Status: Interior of Building 8 finishes are underway, including flooring, ceilings and bathroom tile work. In Building 9, the metal building sheathing is complete, interior walls are complete and finishes have started. Project has been delayed due to several outstanding RFI's regarding design issues and long lead electrical items.

The project is anticipated to be completed late October 2023.



• Howard MS (Comprehensive Renovation)

Notice-to-Proceed was issued on June 12, 2023. Comprehensive renovation and remodeling of the entire campus to provide improved facilities meeting the Design Guidelines and educational program requirements. The project scope includes all renovations needed to address current deficiencies and upgrade all building and site facilities, systems, and finishes at or near the end of their useful life. The project will be completed in four phases.

Phase 1: Anticipated completion early-August 2024.

- Phase 2: Anticipated completion early-August 2025.
- Phase 3: Anticipated completion late-November 2025.
- Phase 4: Anticipated completion early-December 2025.

Project Status: Demolition of retaining wall and install of temporary fence is complete. Conduits and sewer lines for temporary portables is also complete. The install of 11 swing portables is underway. Portables are required as swing space for future interior phases of construction.

The project is anticipated to be completed early December 2025.





727.520.8181 www.aerophoto.com Howard Middle School 21-CM-19

Image # 00 Date 08.31.23

Four (4) New Relief Projects:

• Site 129-M-SE-2 (Laureate Park) (Greenfield school)

Project Status: The Project is moving along on schedule. Tilt wall install is complete. Structural steel has begun.

The project is anticipated to be completed late June 2024.





Site 129-M-SE-2 M.S. Relief 8-21-23



Site 47-E-W-4 (Horizon West Area) (Greenfield school) (Early Procurement Package)
 This project includes construction of a new prototype elementary school building with
 classrooms, administration, art, music, kitchen, cafeteria/multi-purpose room, media center
 and related site work. This elementary school will be designed for 830 student stations.

 Project Status: Notice to Proceed was issued on March 9, 2023 for early procurement of long
 lead items. Site mobilization began with silt and temporary fence and ground clearing in late August.

The project is anticipated to be completed in a single phase, in late June 2024.



Water Spring MS (Site 65-M-W-4) (Horizon West Area MS Relief) (Greenfield school)
 Project Status: Substantial completion achieved. Punch list and close out is underway.





Water Spring MS Winter Garden, FL Image # 6658 Date: 07.25.23 1.800.723.7425

• Site 50-H-SE-2 (Innovation Way Area Northwest) (Greenfield school)

Phase 1: Includes construction of Building 100. Anticipated completion early July 2024.

Phase 2: Includes construction of Building 200. Anticipated completion mid-July 2024.

Project Status: Project is progressing on schedule. Tilt panels have been erected. Structural steel and roof decking is 95% complete. Roofing lightweight concrete and roof membrane has started on Building 100. Interior fire proofing, insulation and MEP rough-outs along with the third floor framing has started in Building 100. Sanitary and deep underground storm piping is completed in parking areas. Grading of parking lots has also begun.



CORE HORUS

SITE 50-H-SE-2 HIGH SCHOOL

08/23/23 Image #01

Two (2) Replacement Projects:


• Site 73-T-W-7 – Orange Technical College / West Campus (Westside):

Project Status: Project is moving along on schedule. Clearing of the roadway on the South side of the project boundary has started. Tilt panels are complete. Structural steel is complete. Second floor concrete deck is poured. Lightweight concrete has begun on the roof along with roof membrane. Framing of interior walls on the first floor and layout of interior walls on the second floor is well underway.

The project is anticipated to be completed late February 2024.









• Site 512-T-E-1 – Orange Technical College / East Campus:

This project is the replacement of the existing campus in Winter Park. The new campus will be located on the site of University HS. The scope of work will include the demolition of the existing Ninth Grade Center. Project consists of a new three story, 102,000 SF building. Programs to be located at this facility include Arts, AV Technology & Communications, Business Management & Administration, and Information Technology.

Project Status: Construction Manager has mobilized and demolition of former Ninth Grade Center is complete. The building pad is complete and foundations are underway.

The project is anticipated to be completed mid December 2024.





Orange Technical College (OTC) East Campus 8.21.23



We currently have 30 projects in the planning or design phase:

PLANNING

- Site 136-A-E-5 (NE Maintenance)
- Boone HS
- Chain of Lakes MS
- Clarcona ES (Old) Demolition
- Esteem Academy
- Jones HS
- Kaley ESE Services
- Lawton Chiles ES
- NorthLake Park ES
- Oakshire ES
- Ocoee MS
- Odyssey MS
- Olympia HS
- Palmetto ES
- Timber Creek HS
- Timber Creek MS

DESIGN

- Site 97-E-SE-2 ICP/West Innovation Way Area ES
- Site 121-A-W-7 West Bus Compound
- Site 130-E-SE-2 Laureate Park Area ES
- Cherokee School
- Colonial HS
- Four Site SY 2024-25
- Four Site SY 2024-25
- Lakeview MS
- Multiple Sites
- Oak Ridge HS
- Orange Technical College / South Campus (Mid-Florida)
- Three Points ES
- Windermere HS (On Site Stadium)
- Winter Park HS

(Replacement) (Comprehensive) (Comprehensive) (Repurpose) (Multi System Renewal) (Comprehensive) (Multi-System Renewal) (Comprehensive) (Comprehensive) (Comprehensive) (Comprehensive)

- (Comprehensive) (Comprehensive)
- (Comprehensive)
- (Comprehensive)
- (Greenfield School) (Repurpose) (Greenfield School) (Repurpose) (Comprehensive) (ES Functional Equity) (MS Functional Equity) (Comprehensive) (Comprehensive) (Comprehensive) (Comprehensive) (Comprehensive) (Greenfield) (Comprehensive)

SINCE LAST REPORT

- Substantial Completion achieved: Water Spring MS (Site 65-M-W-4)
- Notice to Proceed issued: Howard MS, Site 47-E-W-4 (Horizon West Area ES) and Site 512-T-E-1 – Orange Technical College / East Campus

CLOSEOUT

• Water Spring MS

Capital Renewal Update as of September 20, 2023

There are 58 active projects (33 large, 13 intermediate, 12 small) currently in progress for improvements at 108 sites.

Planning

We currently have 10 projects in planning at 36 sites. These include 4 large projects, 5 intermediate projects, and 1 small projects. Since last report, five new projects commenced planning which include canopy and elevated walkway repairs at Dr. Phillips HS; chiller coil replacement at 3 sites; carpet replacement at 14 sites; youth and tot lot replacement at Rosemont ES; and reroofing at Union Park MS. Additionally, a multi-site multi-system improvement project moved to design and two projects moved to construction; an audio enhancement intercom pilot and an HVAC improvement project at NW Maintenance (Old Maxey).

<u>Design</u>

We currently have 23 projects in design at 76 sites. These include 20 large, 2 intermediate, and 1 small projects. Since last report, a multi-site multi-system improvement project moved from planning and a plumbing project at Liberty MS moved to close-out.

Construction

We currently have 25 projects in construction at 51 sites. These include 9 large, 6 intermediate and 10 small projects. This includes 10 chiller projects at various locations in different stages of completion. Since last report, seven new projects commenced construction; air dampers in buildings 2 and 3 at Edgewater HS; youth lot carpet replacement at Lake Silver ES; intercom replacement at OCPS ACE; youth and tot lot replacement at Pinewood ES; tot lot replacement at Washington Shores PLC; LED exterior lighting at Wekiva HS; and youth and tot lot replacement at Windy Ridge K8. Two projects moved from planning to construction; an audio enhancement intercom pilot and an HVAC improvement project at NW Maintenance (Old Maxey). Four projects moved to close-out; parking lot restoration at Boone HS; roofing at Lakeview MS; intrusion detection at 5-sites; and flooring at Riverdale ES. Additionally, a smoke vent repair project at Timber Creek HS moved to Closed.

Capital Renewal Update as of September 20, 2023 Changes since June 15, 2023

<u>Planning</u>

- New Projects
 - o Dr Phillips HS (Canopy/ Elevated Walkway Repairs) N0188.0
 - FY23 Multi-Site Chiller Coil Repl. N0189.0
 - FY24 Multi-Site Carpet Replacement N0190.0
 - Rosemont ES (Youth & Tot Lots) N0090.0
 - Union Park MS (Reroofing) N0191.0
- Moved to Design
 - Multi-System Group 1– N0142.0
- Moved to Construction
 - Audio Enhancement Intercom Pilot N0180.0
 - NW Maint (Old Maxey) HVAC– N0173.0

<u>Design</u>

- Moved from Planning
 - Multi-System Group 1– N0142.0
- Moved to Close-Out
 - Liberty MS (Plumbing) N0141.0

Construction

- New Projects
 - Edgewater HS (Bldg 2 & 3 Air Dampers) N0175.0
 - Lake Silver ES (Youth Lot Carpet) N0181.0
 - OCPS ACE (Intercom Replacement) N0186.0
 - Pinewood ES (Youth & Tot Lots) N0179.0
 - Washington Shores PLC (Tot Lot) N0184.0
 - Wekiva HS (LED Exterior Lighting) N0174.0
 - Windy Ridge K8 (Youth & Tot Lots) N0178.0
- Moved from Planning
 - Audio Enhancement Intercom Pilot N0180.0
 - NW Maint (Old Maxey) N0173.0
- Moved to Close-out
 - Boone HS (Parking Lot Restoration) N0031.8
 - Lakeview MS (Roofing) N0102.1
 - FY22 Low Voltage Intrusion Detection at 05-Sites N0161.0
 - Riverdale ES (Flooring 2nd Floor) N0170.0
- Moved to Closed
 - Timber Creek HS (Smoke Vents) N0037.4

Capital Renewal Update as of September 20, 2023 Changes since June 15, 2023

<u>Close-out</u>

- Moved from Construction
 - Boone HS (Parking Lot Restoration) N0031.8
 - Lakeview MS (Roofing) N0102.1
 - FY22 Low Voltage Intrusion Detection at 05-Sites N0161.0
 - Riverdale ES (Flooring 2nd Floor) N0170.0

Active Projects with Construction Cost Exceeding \$10M per Project Site

Apopka High School – Multi-System Capital Renewal Project Estimated Guaranteed Maximum Price: \$12,419,000

<u>Site</u>

• Replacement of pumps and control panel at lift stations.

Exterior

- Repair and replacement of exterior (EIFS) wall system in select areas.
- Reroofing of select buildings.

Heating, Ventilating and Air Conditioning (HVAC) Renovations

- Refurbishment of existing air handling units (AHUs) and the addition of bi-polar ionization.
- Replacement of the existing building automation system (BAS) components.
- Replacement of exhaust fans, outside air dampers, variable frequency drives (VFDs), electric heating coils, and selected variable air volume (VAV) boxes.
- Selective replacement of Dx and mini-split A/C units and connection to the BAS controls.

Electrical

- Electrical power modifications/upgrades to support the HVAC system design.
- Repair of lightning protection system.
- Replacement of parking lot light fixtures with LED type fixtures.

Life Safety

• Replacement of fire alarm system.

Active Projects with Construction Cost Exceeding \$10M per Project Site

Ocoee High School – Chiller Replacement-HVAC Capital Renewal Project Estimated Guaranteed Maximum Price: \$12,396,200

Heating, Ventilating and Air Conditioning (HVAC) Renovations

- Refurbishment or replacement of existing air handling units (AHUs) and the addition of bipolar ionization.
- Replacement of the existing building automation system (BAS), campus-wide.
- Refurbishment of mechanical rooms, including replacement of gauges, sensors, valves and other appurtenances and restoration of insulation.
- Replacement of exhaust fans, outside air dampers, variable frequency drives (VFDs), electric heating coils, and cleaning of all variable air volume (VAV) boxes.
- Equipment resizing and reengineered air flow requirements.
- Selective replacement of Dx and mini-split A/C units.

Chiller Replacement

- Replacement of existing chillers, cooling towers, and associated pumps, piping, and equipment.
- Reuse of existing controllers.
- Equipment resizing based on load modifications.
- Provision of a new refrigerant leak detection system.

Electrical

- Electrical power modifications/upgrades to support the HVAC system design and new aircooled chillers.
- Reuse of existing feeders or breakers and replacement as needed.

Active Projects with Construction Cost Exceeding \$10M per Project Site

Piedmont Lakes Middle School – Mechanical-HVAC Capital Renewal Project Estimated Guaranteed Maximum Price: \$15,700,000

Heating, Ventilating and Air Conditioning (HVAC) Renovations

- Replacement of the existing building automation system (BAS), campus-wide.
- Redesign of a new Air Distribution System campus-wide per the latest Design Guidelines inclusive of all associated equipment and accessories.
- Conversion of kitchen units from Direct Expansion Cooling (Dx) to Chilled Water.
- Replacement of existing wall mounted mini-split system in select areas.
- Evaluation of all IDF and CCTV rooms current heat load requirements to include with the new Air Distribution System.

Plumbing

- Replacement of approximately 400 LF of underground sanitary sewer line.
- Replacement of all hot water heaters.

Electrical

• Installation of Power and data ports for building automation system (BAS) interconnectivity and new electrical circuitry as required to support all new equipment installation.

Interior

• Replacement of finishes as needed to accommodate new design.

Active Projects with Construction Cost Exceeding \$10M per Project Site

Roberto Clemente Middle School – Multi-System Capital Renewal Project Estimated Guaranteed Maximum Price: \$16,300,000

<u>Site</u>

• Correcting drainage issues campus-wide.

Roofing

- Roof replacement of buildings 100, 200, 300, 400 and 700.
- Roof repairs of building 500.

Exterior

- Select door replacement.
- Replace exterior door and window seals.

Interior

- Select door replacement.
- Replacement of finishes as needed to accommodate new design.
- Replacement of serving line equipment.

Heating, Ventilating and Air Conditioning (HVAC) Renovations

- Replace HVAC system equipment in buildings 100, 200, 300, and 500.
- Refurbishment of HVAC system in other buildings.
- Replacement of the existing building automation system (BAS), campus-wide.

Plumbing

• Reconfigure restrooms in building 700 for ADA compliance.

Electrical & Systems

- Electrical upgrades necessary for HVAC work.
- Exterior lighting upgrades to LED.
- Lighting LED upgrade in select buildings.
- Intercom system replacement for entire campus.
- Intrusion detection and security CCTV upgrades campus-wide.

Life Safety

• Fire alarm system interconnection upgrade to fiber.

Active Projects with Construction Cost Exceeding \$10M per Project Site

West Orange High School – HVAC Renovation-HVAC Capital Renewal Project Estimated Guaranteed Maximum Price: \$10,300,000

Heating, Ventilating and Air Conditioning (HVAC) Renovations

- Refurbishment or replacement of existing air handling units (AHUs) and the addition of bipolar ionization.
- Replacement of the existing building automation system (BAS) controls, campus-wide.
- Refurbishment of mechanical rooms, including replacement of gauges, sensors, valves and pumps.
- Replacement of exhaust fans, outside air dampers, variable frequency drives (VFDs), electric heating coils, and selected variable air volume (VAV) boxes.
- Selective replacement of Dx and mini-split A/C units.

Electrical

- Electrical power modifications/upgrades to support the HVAC system design.
- Reuse of existing feeders or breakers, lightning protection system and replacement as needed.

CHANGE ORDERS REPORT

Change Orders Report

Facilities & Construction Contracting June 2023

PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC NO.	AM GMP NO.	DOC NO.	REQUESTED AMOUNT	REASON FOR CHANGE	APPROVAL REQUIREMENT
High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Change Order	21CM07SCON CORE	1	2	\$667,788.70	Increase General Conditions in GMP 1. General Conditions in GMP 6 was reduced by the same amount resulting in an overall no cost change to the project.	Board (6/13/23) / Rory A. Salimbene, Acting Chief Facilities Officer

There are no significant Amendments to the report for the month of June 2023.

COVE Report for June 2023

CONT	RACTS AMEN	DED								
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	APPROVAL REQUIREMENT
1	Elementary School Site 47-E-W-4 [*]	Schenkel & Shultz, Inc.	Design Change Directive	2137SCON001 SCHENKEL	1	\$12,000.00	Architectural & Engineering Services	2137PS	Modifications of design in the multipurpose space to incorporate unisex stalls for new elementary school relief project.	Catherine Sullivan on behalf of Rory A. Salimbene, Acting Chief Facilities Officer
2	High School Site 50-H-SE-2	Zyscovich, LLC	Design Change Directive	2104SCON ZYSCOVICH	3	\$44,000.00	Architectural & Engineering Services	2104PS	Modifications of design in Classroom Building 100, floors I, 2 and 3 to incorporate unisex stalls for new high school relief project.	Rory A. Salimbene, Acting Chief Facilities Officer
3	Legacy MS	OCI Associates, Inc.	Amendment	1514078	1	\$7,510.00	Mechanical, Electrical & Plumbing Engineering Services	1514PS	Additional design services to modify air handling unit fan design to utilize variable frequency drives for HVAC renovation. Capital renewal project.	Catherine Sullivan, Sr. Facilities Manager, Design
4	Middle School Site 129-M-SE-2*	Schenkel & Shultz, Inc.	Design Change Directive	2122SCON SCHENKEL	3	\$46,000.00	Architectural & Engineering Services	2122PS	Design modifications to classroom building, media center, and gymnasium to incorporate unisex stalls for new middle school relief project.	Rory A. Salimbene, Acting Chief Facilities Officer
5	Washington Shores Primary Learning Center	OCI Associates, Inc.	Amendment	1514077	1	\$7,510.00	Mechanical, Electrical & Plumbing Engineering Services	1514PS	Additional design services to modify air handling unit fan design to utilize variable frequency drives for HVAC renovation. Capital renewal project.	Catherine Sullivan, Sr. Facilities Manager, Design

*Not Funded by Sales Tax or Capital Renewal

COVE Report for June 2023

CHAN	GE ORDERS AF	PROVED										
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	AM GMP No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	ODP %	APPROVAL REQUIREMENT
1	Avalon MS & Meadowbrook MS	CORE Construction Services of Florida, LLC	Change Order	20CM06SC ON CORE	2	1	(\$2,953,310.26)	Construction Management Services	20CM06	Estimated ODP. Capital renewal project.		Rory A. Salimbene, Acting Chief Facilities Officer
2	Dr. Phillips HS	H. A. Contracting Corp.	Change Order	19CM09029 B		1	(\$718,441.07)	Construction Management Services	19CM09	Estimated ODP for north campus. Multi- system, Capital renewal project.		Craig Jackson on behalf of Rory A. Salimbene, Acting Chief Facilities Officer
3	East River HS [*]	Sequel Developers, Inc.	Construction Change Directive	19CM09027 B		1	\$50,000.00	Construction Management Services	19CM09	Cost to deliver, place, and grade additional imported fill material for new athletic practice field. District capital project.		Rory A. Salimbene, Acting Chief Facilities Officer
4	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Change Order	21CM07SC ONCORE	4	2	\$111,081.25	Construction Management Services	21CM07	Cost resulting from the revised location of the OUC service entry point for new school relief project.		Superintendent / Rory A. Salimbene, Acting Chief Facilities Officer
5	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Change Order	21CM07SC ON CORE	5	2	(\$427,330.00)	Construction Management Services	21CM07	Removal of "Alternate No. 2 – Exterior Sun Shade Devices" scope of work from the contract documents for new school relief project.		Superintendent / Rory A. Salimbene, Acting Chief Facilities Officer

COVE Report for June 2023

CHAN	CHANGE ORDERS APPROVED													
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	AM GMP No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	ODP %	APPROVAL REQUIREMENT		
6	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Change Order	21CM07SC ON CORE	1	2	\$667,788.70	Construction Management Services	21CM07	Increase General Conditions in GMP 1. General Conditions in GMP 6 was reduced by the same amount resulting in an overall no cost change to the project.		Board (6/13/23) / Rory A. Salimbene, Acting Chief Facilities Officer		
7	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Construction Change Directive	21CM07SC ON CORE	6	1	\$0.00	Construction Management Services	21CM07	Partial use of Allowance (\$1,050,200 of the \$5,500,000) included in the GMP for procurement of schedule critical long lead items.		Craig A. Jackson, Sr. Construction Director		
8	Jones HS [*]	McCree Design Builders, Inc.	Change Order	19CM09010 B		1	(\$886,589.53)	Construction Management Services	19CM09	Estimated ODP.		Craig Jackson on behalf of Rory A. Salimbene, Acting Chief Facilities Officer		
9	Middle School Site 129-M-SE-2 [*]	Walker & Company, Inc.	Construction Change Directive	21CM23SC ON WALKER	1	1	\$0.00	Construction Management Services	21CM23	Use of \$500,000 allowance included in the early GMP to purchase main distribution panel switchboards for new relief project.		Craig A. Jackson, Sr. Construction Director		

COVE Report for June 2023

CHANGE ORDERS APPROVED													
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	AM GMP No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	ODP %	APPROVAL REQUIREMENT	
10	Orange Technical College - West Campus 73-T-W-7	Wharton- Smith, Inc.	Change Order	19CM05SC ON WHARTON	2	2	\$45,003.00	Construction Management Services	19CM05	Time extension of 34 days to relocate gopher tortoises resulting in added General Conditions and recipient site fees for new school replacement project.		Rory A. Salimbene, Acting Chief Facilities Officer	
11	Panther Lake ES 114-E-W-4 [*]	Williams Company Building Division, Inc.	Change Order	20CM10SC ON WILLIAMS	1	11	\$0.00	Construction Management Services	20CM10	Time extension of 154 days for Phase 3 - traffic signalization due to manufacturing delays associated with mast arms, traffic control equipment, and Duke Energy providing power to traffic equipment for prototype new school relief project.		Board (6/13/23) / Rory A. Salimbene, Acting Chief Facilities Officer	
12	Various Schools Rubberized Track Program [*]	Wharton- Smith, Inc.	Change Order	18CM20SC ON WHARTON	1	5	\$422,426.25	Construction Management Services	18CM20	ODP reconciliation for district capital project.		Rory A. Salimbene, Acting Chief Facilities Officer	

*Not Funded by Sales Tax or Capital Renewal

Change Orders Report

Facilities & Construction Contracting July 2023

There are no significant change orders or amendments to the report for the month of July 2023.

COVE Report for July 2023

CONT	RACTS AMEN	DED								
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	APPROVAL REQUIREMENT
1	Howard MS	Terracon Consultants, Inc.	Amendment	1717164	3	\$7,652.85	Environmental Consulting Services	1717PS	Additional pre-demolition surveying to comply with National Emissions Standards for Hazardous Air Pollutants for air monitoring inside and outside the work area during the abatement process for a comprehensive project.	Catherine Sullivan, Sr. Facilities Manager, Design
2	Hungerford ES Building 8 Renovation	Schenkel & Shultz, Inc.	Design Change Directive	1816SCON001 SCHENKEL	1	\$0.00	Architectural & Engineering Services	1816PS	Design Change Directive for electrical scope revisions for the comprehensive project.	Catherine Sullivan, Sr. Facilities Manager, Design
3	Middle School Site 129-M-SE-2 [*]	Professional Service Industries, Inc.	Amendment	1517315	1	\$1,304.95	Geotechnical & Environmental Services	1517PS	Additional observation and inspection of excavated material in building pad/foundation areas for prototype new school relief project.	Catherine Sullivan, Sr. Facilities Manager, Design

*Not Funded by Sales Tax or Capital Renewal

COVE Report for July 2023

CHAN	GE ORDERS /	APPROVED										
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	AM GMP No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	ODP %	APPROVAL REQUIREMENT
1	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Construction Change Directive	21CM07SC ON CORE	4	1	\$57,400.00	Construction Management Services	21CM07	Modification to group restrooms on second and third floors of Building 100 to provide eight private unisex stalls within GMP of the new school relief project.		Superintendent / Rory A. Salimbene, Chief Facilities Officer
2	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Construction Change Directive	21CM07SC ONCORE	5	1	\$88,800.00	Construction Management Services	21CM07	Modification to group restrooms on the first floor of Building 100 to provide four private unisex stalls within GMP 5 of the new school relief project.		Superintendent / Rory A. Salimbene, Chief Facilities Officer
3	High School Site 50-H-SE-2	CORE Construction Services of Florida, LLC	Construction Change Directive	21CM07SC ON CORE	5	2	\$113,600.00	Construction Management Services	21CM07	Modification of group restrooms on second and third floors of Building 100 to provide eight private unisex stalls within GMP 5 of the new school relief project.		Superintendent / Rory A. Salimbene, Chief Facilities Officer
4	Howard MS	LEGO Construction Co.	Change Order	21CM19SC ON LEGO	1	1	(\$10,662,670.08)	Construction Management Services	21CM19	Estimated ODP for the comprehensive project.		Craig Jackson on behalf of Rory Salimbene, Chief Facilities Officer

COVE Report for July 2023

CHAN	GE ORDERS	APPROVED										
ITEM NO.	PROJECT NAME	VENDOR NAME	DOCUMENT TYPE	ORIGINAL DOC No.	AM GMP No.	DOC No.	REQUESTED AMOUNT	SERVICE TYPE	RFQ No.	REASON FOR CHANGE	ODP %	APPROVAL REQUIREMENT
5	Orange Technical College - East Campus 512-T-E-1	Charles Perry Partners, Inc.	Change Order	20CM18SC ON CHARLES	4	1	(\$10,973,569.00)	Construction Management Services	20CM18	Estimated ODP for new school replacement project.		Craig Jackson on behalf of Rory Salimbene, Chief Facilities Officer
6	Panther Lake ES 114-E-W-4 [*]	Williams Company Building Division, Inc.	Change Order	20CM10SC ON WILLIAMS	1	12	(\$372,386.86)	Construction Management Services	20CM10	Final GMP reconciliation for prototype new school relief project.		Rory A. Salimbene, Chief Facilities Officer

*Not Funded by Sales Tax or Capital Renewal

OCPS FACILITIES & CONSTRUCTION CONTRACTING

RFQs in Progress: SEPTEMBER 2023

No.	Contract Description	Pre Submittal Meeting	Open Date	Shortlist Meeting	Interview Meeting	Board / CFO Date	Construction Budget	Firm(s) Awarded	Status
RFQ 2312PS	A/E Services for Chain of Lakes MS Comprehensive Renovation Project	9/19/2023	10/10/2023	10/17/2023	10/31/2023		\$ 38,000,000.00		On-Going
RFQ 2313CM	CM Services for Chain of Lakes MS Comprehensive Renovation Project	9/19/2023	10/11/2023	10/24/2023	11/7/2023		\$ 38,000,000.00		On-Going
RFQ 2314PS	A/E Services for Timber Creek HS Comprehensive Renovation Project	10/6/2023	10/17/2023	10/25/2023	11/14/2023		\$ 92,382,000.00		On-Going
RFQ 2315CM	CM Services for Timber Creek HS Comprehensive Renovation Project	10/6/2023	10/18/2023	11/1/2023	11/15/2023		\$ 92,382,000.00		On-Going

HOWARD MS COMPREHENSIVE RENOVATION

CAPITAL RENEWAL FUNDING FORMULA

Discussion Topics

- 1. Orange's Half-Penny Sales Tax Scott Howat
- 2. Next COVE meeting scheduled for Thursday, October 19, 2023.

NOTES



GLOSSARY OF TERMS

Funding Source Descriptions

CIT - **Capital Improvement Tax:** Funds derived from a 1.5 millage levy on local property. Revenues maybe used for payment of principal and interest on COPS, for purchase of new and replacement equipment; for maintenance of existing facilities; rental and leasing of educational facilities and sites; purchase of new and replacement school buses; project management and for construction and remodeling of new or existing facilities. Based on 2017 legislation, a portion of the funds derived from the capital improvement millage may be distributed to eligible charter schools to pay for capital needs including but not limited to construction, vehicle purchases, and real property acquisition.

COPS - Certificates of Participation: These funds are not a source of revenue but the proceeds of a twentyfive year loan against future property tax revenues. Funds may be used to remodel, renovate or replace existing schools and acquire land and construct additional schools.

CSR - **Class Size Reduction:** The voter approved constitutional amendment placed the responsibility for providing the necessary operating and capital funds required on the Legislature. The Class Size Reduction Capital Outlay program was established to provide funds to eligible public school districts for capital outlay purposes to reduce class size or for any lawful capital outlay purpose if the class size maximum had been met. In fiscal year 2000, the district received \$147.7 million from this program.

IMPACT - School Impact Fees: Florida Statutes direct local governments to make efficient and adequate provisionsfor schools. Impact fees represent a total or partial reimbursement for the cost of additional facilities or services necessary as a result of the new development. Funds can only be used to pay for capital expenditures resulting from student growth (i.e. relief schools).

QSCB - **Qualified School Construction Bonds:** QSCBs are financial instruments that provide a subsidy in the form of a tax credit to a bank or other financial institution that holds the QSCBs. The tax revenues are made available by the federal government to help fund school construction, rehabilitation, repair and land acquisition. These bonds were authorized by the federal government through the American Recovery and Reinvestment Act (ARRA) of 2009.

SIT - **School Infrastructure Thrift Award:** The SIT program provided incentive grants to districts for savings realized through functional and frugal school construction. These awards were funded by the Educational Enhancement (Lottery) Trust Fund. The district received a total of \$22.2 million for qualifying capital expenses.

Common Terms by OCPS Facilities

AE - Architect/ Engineer

BAS - Building Automation System

BIC - Ball-in-court

BOS - **Bill of Sale:** Utility providers may require a sketch, legal description, and / or a bill of sale (documentation of sale of transfer of goods) for infrastructure improvements performed by the construction contractor.

CCD - Construction Change Directive

CCTV - Closed Circuit Television

CFI - Certificate of Final Inspection

CM - Construction Manager

CO - Change Order

CR - Contingency Request: GMP contract Amendments include not-to-exceed values for Contractor's Contingency and Owner's Contingency. Both require Owner approval prior to use.

DX - **Direct Expansion:** Direct expansion cooling is a type of refrigerant based HVAC system.

ES - Elementary School

FISH - Florida Inventory of School Houses: The Florida Department of Education maintains a central database of information for all educational and non-instructional facilities throughout the state.

FY - Fiscal Year

GC - General Contractor

GMP - Guaranteed Maximum Price

GR - **General Requirements:** GMP contract amendments include not-to-exceed values for Contractor reimbursable expenses that are not directly related to the construction cost of the work.

HS - High School

HVAC - Heating, Ventilation, and Air Conditioning

IDF - **Intermediate Distribution Frame:** IDF rooms are utilized for secondary distribution of networking systems throughout the facility.

Common Terms by OCPS Facilities

INT - Intermediate: Projects with construction costs between \$280,000 and \$2,000,000.

LF – Linear Foot

LG - Large: Projects with construction costs that exceed \$2,000,000.

MDF - **Main Distribution Frame:** MDF rooms are utilized for primary distribution of networking systems throughout the facility.

MS - Middle School

NTP - Notice to Proceed

O&M - Operation and Maintenance

ODP - **Owner Direct Purchase:** The ODP program allows the District to benefit from its tax-exempt status by directly purchasing materials from suppliers, thereby avoiding the sales tax that contractors purchasing the same materials would pay.

PM TEAM - Program Management Team

REPL - Replacement

SERV - Service

SF - Square Foot

SM - Small: Projects with construction costs less than \$280,000.

SUBST - Substantial

SY - School Year

TBD - To Be Determined

TCO - Temporary Certificate of Occupancy

WIP - Work in Progress

Wt'd Age - Weighted Age: The weighted age of a facility is the average number of years since construction or comprehensive renovation. When buildings on a campus have different ages, an average is determined using the net floor area as the weighting factor.
